

MSR10

(NUMBER TO BE ASSIGNED BY STATE)

APPLICANT IS THE:  OWNER  PRIME CONTRACTOR

OWNER CONTACT INFORMATION

OWNER CONTACT PERSON: Robert Goodman
OWNER COMPANY LEGAL NAME: Lotus Pines LLC
OWNER STREET OR P.O. BOX: 1317 Edgewater Drive Suite 5504
OWNER CITY: Orlando STATE: FL ZIP: 32804
OWNER PHONE #: (917) 744-3688 OWNER EMAIL: rgoodman@mac.com

PREPARER CONTACT INFORMATION

r.goodman@mac.com

IF NOI WAS PREPARED BY SOMEONE OTHER THAN THE APPLICANT
CONTACT PERSON: Lucas Leeper
COMPANY LEGAL NAME: Engineering Plus, Inc.
STREET OR P.O. BOX: 1724-B 23rd Avenue
CITY: Meridian STATE: MS ZIP: 39301
PHONE #: ( ) 601-693-4234 EMAIL: lucasl@engineeringplus.com

PRIME CONTRACTOR CONTACT INFORMATION

PRIME CONTRACTOR CONTACT PERSON: Michael Mayerhoff
PRIME CONTRACTOR COMPANY LEGAL NAME: Davidson Hauling
PRIME CONTRACTOR STREET OR P.O. BOX: P.O. Box 665
PRIME CONTRACTOR CITY: Marion STATE: MS ZIP: 39342
PRIME CONTRACTOR PHONE #: (601) 934-6987 PRIME CONTRACTOR EMAIL: mm@dvdson.net

FACILITY SITE INFORMATION

FACILITY SITE NAME: The Pines of Meridian
FACILITY SITE ADDRESS (If the physical address is not available, please indicate the nearest named road. For linear projects indicate the beginning of the project and identify all counties the project traverses.)
STREET: 1921 Russell Mt Gilead Road
CITY: Meridian STATE: MS COUNTY: Lauderdale ZIP: 39301
FACILITY SITE TRIBAL LAND ID (N/A If not applicable): NA
LATITUDE: 32 degrees 24 minutes 15.14 seconds LONGITUDE: 88 degrees 35 minutes 22.79 seconds
LAT & LONG DATA SOURCE (GPS (Please GPS Project Entrance/Start Point) or Map Interpolation): google earth
TOTAL ACREAGE THAT WILL BE DISTURBED: 13

IS THIS PART OF A LARGER COMMON PLAN OF DEVELOPMENT? YES  NO

IF YES, NAME OF LARGER COMMON PLAN OF DEVELOPMENT: \_\_\_\_\_  
 AND PERMIT COVERAGE NUMBER: MSR10 \_\_\_\_\_

ESTIMATED CONSTRUCTION PROJECT START DATE: 2026-05-18  
 YYYY-MM-DD

ESTIMATED CONSTRUCTION PROJECT END DATE: 2026-09-30  
 YYYY-MM-DD

DESCRIPTION OF CONSTRUCTION ACTIVITY: Clearing, grading, and construction of an RV park including pads, utilities, and access drives.

PROPOSED DESCRIPTION OF PROPERTY USE AFTER CONSTRUCTION HAS BEEN COMPLETED:  
RV park with stabilized pads, access drives, utilities, and associated site improvements.

SIC Code: 7033 NAICS Code 721211

NEAREST NAMED RECEIVING STREAM: Nanabe Creek

IS RECEIVING STREAM ON MISSISSIPPI'S 303(d) LIST OF IMPAIRED WATER BODIES? (The 303(d) list of impaired waters and TMDL stream segments may be found on MDEQ's web site: [http://www.deq.state.ms.us/MDEQ.nsf/page/TWB\\_Total\\_Maximum\\_Daily\\_Load\\_Section](http://www.deq.state.ms.us/MDEQ.nsf/page/TWB_Total_Maximum_Daily_Load_Section)) YES  NO

HAS A TMDL BEEN ESTABLISHED FOR THE RECEIVING STREAM SEGMENT? YES  NO

FOR WHICH POLLUTANT:

ARE THERE RECREATIONAL STREAMS, PRIVATE/PUBLIC PONDS OR LAKES WITHIN 1/2 MILE DOWNSTREAM OF PROJECT BOUNDARY THAT MAY BE IMPACTED BY THE CONSTRUCTION ACTIVITY? YES  NO

EXISTING DATA DESCRIBING THE SOIL (for linear projects please describe in SWPPP):  
Soil on this property classify as fine sandy loams and Sweatman association using NRCS information.

WILL FLOCCULANTS BE USED TO TREAT TURBIDITY IN STORM WATER? YES  NO

IF YES, INDICATE THE TYPE OF FLOCCULANT.  ANIONIC POLYACRYLIMIDE (PAM)  
 OTHER \_\_\_\_\_

IF YES, DOES THE SWPPP DESCRIBE THE METHOD OF INTRODUCTION, THE LOCATION OF INTRODUCTION AND THE LOCATION OF WHERE FLOCCULATED MATERIAL WILL SETTLE?

IS A SDS SHEET INCLUDED FOR THE FLOCCULATE? YES  NO

WILL THERE BE A 50 FT BUFFER BETWEEN THE PROJECT DISTURBANCE AND THE WATERS OF THE STATE? YES  NO

IF NOT, PROVIDE EQUIVALENT CONTROL MEASURES IN THE SWPPP.

<sup>1</sup>Acreage for subdivision development includes areas disturbed by construction of roads, utilities and drainage. Additionally, a housesite of at least 10,000 ft<sup>2</sup> per lot (entire lot, if smaller) shall be included in calculating acreage disturbed.

**DOCUMENTATION OF COMPLIANCE WITH OTHER REGULATIONS/REQUIREMENTS**  
 COVERAGE UNDER THIS PERMIT WILL NOT BE GRANTED UNTIL ALL OTHER REQUIRED  
 MDEQ PERMITS AND APPROVALS ARE SATISFACTORILY ADDRESSED

IS LCNOI FOR A FACILITY THAT WILL REQUIRE OTHER PERMITS?

YES  NO

IF YES, CHECK ALL THAT APPLY:  AIR  HAZARDOUS WASTE  PRETREATMENT  
 WATER STATE OPERATING  INDIVIDUAL NPDES  OTHER: \_\_\_\_\_

IS THE PROJECT REROUTING, FILLING OR CROSSING A WATER CONVEYANCE OF ANY KIND? (If yes, contact the U.S. Army Corps of Engineers' Regulatory Branch for permitting requirements.) YES  NO

IF THE PROJECT REQUIRES A CORPS OF ENGINEER SECTION 404 PERMIT, PROVIDE APPROPRIATE DOCUMENTATION THAT:

- The project has been approved by individual permit, or
- The work will be covered by a nationwide permit and NO NOTIFICATION to the Corps is required, or
- The work will be covered by a nationwide or general permit and NOTIFICATION to the Corps is required

IS THE PROJECT REROUTING, FILLING OR CROSSING A STATE WATER CONVEYANCE OF ANY KIND? (If yes, please provide an antidegradation report.) YES  NO

IS A LAKE REQUIRING THE CONSTRUCTION OF A DAM BEING PROPOSED? (If yes, provide appropriate approval documentation from MDEQ Office of Land and Water, Dam Safety.) YES  NO


IF THE PROJECT IS A SUBDIVISION OR A COMMERCIAL DEVELOPMENT, HOW WILL SANITARY SEWAGE BE DISPOSED? Check one of the following and attach the pertinent documents.

- Existing Municipal or Commercial System. Please attach plans and specifications for the collection system and the associated "Information Regarding Proposed Wastewater Projects" form or approval from County Utility Authority in Hancock, Harrison, Jackson, Pearl River and Stone Counties. If the plans and specifications can not be provided at the time of LCNOI submittal, MDEQ will accept written acknowledgement from official(s) responsible for wastewater collection and treatment that the flows generated from the proposed project can and will be transported and treated properly. The letter must include the estimated flow.
- Collection and Treatment System will be Constructed. Please attach a copy of the cover of the NPDES discharge permit from MDEQ or indicate the date the application was submitted to MDEQ (Date: \_\_\_\_\_.)
- Individual Onsite Wastewater Disposal Systems for Subdivisions Less than 35 Lots. Please attach a copy of the Letter of General Acceptance from the Mississippi State Department of Health or certification from a registered professional engineer that the platted lots should support individual onsite wastewater disposal systems.
- Individual Onsite Wastewater Disposal Systems for Subdivisions Greater than 35 Lots. A determination of the feasibility of installing a central sewage collection and treatment system must be made by MDEQ. A copy of the response from MDEQ concerning the feasibility study must be attached. If a central collection and wastewater system is not feasible, then please attach a copy of the Letter of General Acceptance from the State Department of Health or certification from a registered professional engineer that the platted lots should support individual onsite wastewater disposal systems.

INDICATE ANY LOCAL STORM WATER ORDINANCE (I.E. MS4) WITH WHICH THE PROJECT MUST COMPLY:

\_\_\_\_\_  
 \_\_\_\_\_

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.



Signature of Applicant<sup>1</sup> (owner or prime contractor)

5/1/2026

Date Signed

ROBERT GOODMAN

Printed Name<sup>1</sup>

PRESIDENT

Title

<sup>1</sup>This application shall be signed as follows:

- For a corporation, by a responsible corporate officer.
- For a partnership, by a general partner.
- For a sole proprietorship, by the proprietor.

For a municipal, state or other public facility, by principal executive officer, mayor, or ranking elected official

Please submit the LCNOI form to:

Chief, Environmental Permits Division  
MS Department of Environmental Quality, Office of Pollution Control  
P.O. Box 2261  
Jackson, Mississippi 39225

Electronically:

<https://www.mdeq.ms.gov/construction-stormwater/>

Revised 3/23/22

# Engineering Plus

Planning – Surveying – Testing – Landscape Design

May 1<sup>st</sup> 2026

Carrie Barefoot  
401/Stormwater Branch  
Environmental Permits Division  
MS Department of Environmental Quality, Office of Pollution Control  
P.O. Box 2261  
Jackson, MS 39225

RECEIVED

MAY 06 2026

Dept. of Environmental Quality

**RE:    *The Pines of Meridian – Meridian, MS  
      Large Construction Notice of Intent Package***

Dear Ms. Barefoot:

Lotus Pines LLC is preparing to develop a parcel of land for a future RV Park by performing clearing and grubbing and grading to include pads, utilities, and access drives as part of their initial construction. Prior to any ground disturbing activities, such as clearing and grubbing, we are requesting permit coverage from your office.

Please find enclosed, for your review, a Stormwater Pollution Prevention Plan that includes a Large Construction General Permit Package with required owner signatures. The package also includes other pertinent information for your review.

Thank you for your consideration in this matter. Please contact us if you have any questions or need additional information for this application.

Respectfully,



Lucas Leeper, P.E.  
Project Engineer

Enclosures: As noted

# **Storm Water Pollution Prevention Plan**

## **The Pines of Meridian Clearing and Grubbing and Initial Site Grading Meridian, Mississippi**

**Prepared For:  
Lotus Pines, LLC  
Orlando, FL**

**Prepared By:  
Engineering Plus, Inc.  
1724-B 23<sup>rd</sup> Avenue  
Meridian, MS 39301**

**May 2026**

---

## TABLE OF CONTENTS

Introduction	2
Site Description	2
General Requirements	3
Best Management Practices	3
Housekeeping Practices	4
Implementation Sequence	4
Post Construction/Storm Water Management Measures	4
Inspection/Maintenance	5
Staff Training Requirements	5
MDEQ Large Construction Notice of Intent & General Permit Package	
Best Management Standards	
Site Location Map	
Quad Map	
Soil Survey of Lauderdale County, MS	
Erosion Control Plan	

## **INTRODUCTION**

This document is the Storm Water Pollution Prevention Plan (SWPPP) for proposed site clearing and grubbing and initial site grading on a parcel of land along Highway 11&80 Meridian, Mississippi. This plan is the criteria for compliance with the regulation set by the Environmental Protection Agencies National Pollutant Discharge Elimination System permit application regulations for storm water discharges regarding construction storm water. The purpose of the Storm Water Pollution Prevention Plan is for the control and mitigation of pollution in storm water discharges associated with the proposed project.

## **SITE DESCRIPTION**

This project consists of clearing, grubbing, and site grading for RV pads, internal access drives, utility installation, and onsite wastewater (mound) systems at the proposed RV park site located at the intersection of Russell Mt. Gilead Road and Highway 11 & 80 in the Russell Community. Topsoil will be stockpiled and reused for final stabilization of disturbed areas. Best management practices (BMPs) will be installed and maintained in accordance with the attached Erosion Control Plan prior to and during construction. Disturbed areas will be stabilized as work progresses, with final stabilization achieved through permanent vegetation and aggregate surfacing as applicable. Existing drainage features, including a ditch traversing the central and northern portions of the site, will be maintained. Based on site topography, drainage patterns, and disturbed acreage, sediment basins are not anticipated to be required; erosion and sediment control will be achieved through perimeter controls, check structures, and phased stabilization.

Clearing and grubbing will disturb approximately 13 acres located in the southeast quarter of Section 22, Township 7 North, Range 15 East, Lauderdale County, Mississippi. The topography of the site contains mostly gently sloping areas with the majority of the drainage generally flowing to the central and northern ditch lines on the property. All current stormwater runoff generally flows to Nanabe Creek. From the Soil Survey of Neshoba County, by the Soil Conservation Service, the majority of the existing soils appear to be Jena and Prentiss Fine Sandy Loam and Sweatman association (Ja, PtA, and SW) soils.

The project site described above is currently a wooded area with largely open portions along the center of the property used as site access. The property is not currently being used for any industrial, commercial, agricultural, or residential purposes at this time. As stated above, storm water from this proposed site drains to Nanabe Creek. Nanabe Creek is not listed on the 303(d) list for impairment as prescribed by MDEQ. Nanabe Creek does not show any TMDL's. The controls utilized on-site, as shown in the Erosion Control Plan are sufficient to provide protection from impacting Nanabe Creek Downstream. These controls utilized on-site consists of silt fence and brush barriers. Additional controls are not warranted.

## GENERAL REQUIREMENTS

The Storm Water Pollution Prevention Plan consists of various controls appropriate for this particular site. The purposes of these various controls shall:

- Implement Best Management Practices to reduce adverse effects from storm water runoff.
- Preserve existing vegetation and re-vegetating disturbed soil as soon as possible to limit the exposure time for the disturbed area.
- Remove sediment from storm water before it leaves the site through the use of structural controls.
- Minimize disturbed surface area.
- Prevent sediment from leaving the site by providing construction Best Management Practices throughout the entirety of the project.

## BEST MANAGEMENT PRACTICES

The implementation of these practices is anticipated to begin in May 2026 and end September 2026. The controls of importance include but are not limited to:

- Installation of construction entrance/exit (see Erosion Control Plan).
- Installation of silt fencing and wattles as needed (see Erosion Control Plan).
- Installation of brush barriers as needed (see Erosion Control Plan).
- Construction of temporary diversion berms as needed
- Temporary vegetation to be established throughout the construction.
- Permanent re-vegetation shall occur after clearing and grubbing to prevent erosion. Permanent vegetation is established when the site is at a minimum of 70% stabilization

The prime contractor shall implement controls as needed to prevent erosion and adverse impacts on nearby streams and/or ponds. Vegetative practices shall be designed to preserve existing vegetation where feasible and initiate vegetative stabilization measures after land disturbing activities. Such practices may include, but not limited to, temporary seeding, permanent seeding, mulching, sod stabilization, vegetative buffer strips, tree protection and topsoil preservation. **When work is not being performed in a disturbed area or when a disturbed area is left dormant for fourteen (14) calendar days or more, appropriate temporary and/or permanent vegetative and structural practices shall be initiated immediately.**

## **HOUSEKEEPING PRACTICES**

The owner or prime contractor shall prevent pollutants from entering storm water from the construction site because of poor housekeeping. The owner or prime contractor shall designate areas for equipment maintenance/staging, fueling and repair that are located near the construction entrances. All fueling of equipment and vehicles on the site will be conducted in this area. Any spillage will be removed immediately. All fuel tanks will be kept in containment areas. Oils, other vehicle fluids, paints, solvents and other potentially toxic materials shall be stored in a construction trailer or storage container. The contractor is responsible for providing litter control for trash generated by his/her crew. Waste receptacles, if needed, shall be provided at convenient locations near the construction entrance which will be limited to garbage and paper trash as well as construction debris. Litter and construction debris exposed to storm water shall be picked up prior to any anticipated storm events or before being carried off the site by wind or construction traffic. Sanitary facilities shall be provided by the contractor to collect sanitary waste from his/her crew. These facilities shall be adequately maintained sanitary facilities and shall be emptied at the end of each working week or once they become full, whichever occurs first. Sanitary facilities shall be secured firmly to the ground to prevent wind-blown damage from occurring. Any existing pavements or roadways near the construction entrances shall be cleaned as needed to prevent tracking of sediment off-site. Where sediment has been tracked-out from the site onto adjacent paved roads, sidewalks or other paved areas, the contractor shall remove deposited sediment "immediately" by the end of the next work day. Sediment shall be removed by sweeping, shoveling, vacuuming or similar effective means of sediment removal.

## **IMPLEMENTATION SEQUENCE**

The implementation sequence is as follows:

- Construct the construction entrance/exit.
- Install silt fencing as needed. (To be cleaned after silt build-up)
- Install brush barrier as needed
- Install temporary diversion berms and wattles as needed.
- Perform clearing and grubbing and vegetate as needed.

## **POST CONSTRUCTION/STORM WATER MANAGEMENT MEASURES**

- Remove silt fencing and wattles after satisfactory vegetation cover is in place.
- Remove brush barriers by appropriate means.

## **INSPECTION/MAINTENANCE**

A rain gage shall be set up on-site. Within 24 hours after commencement of a rainfall event of 2 inches or more, an inspection of all erosion controls and other S.W.P.P.P. requirements shall be performed during the permit coverage.

All accumulated sediment shall be removed from structural controls when sediment deposits reach 1/3 to 1/2 the height of the control. Accumulated sediment from the sedimentation pond shall be removed when the sediment reaches 50% capacity of the pond. All removed sediment deposits shall be properly disposed. Non-functioning controls shall be repaired, replaced or supplemented with functional controls within 24 hours of discovery or as soon as field conditions allow.

Make all needed repairs within 24 hours. Maintain all vegetated areas to provide proper ground cover-reseed, fertilize and mulch as needed.

Inspection of all temporary and vegetative, erosion and sediment controls, other protective measures and S.W.P.P.P. requirements shall be performed during permit coverage every seven days with a minimum of four (4) per month and after any rain events that produce a discharge to ensure appropriate erosion and sediment controls are being properly and adequately constructed and maintained. These inspections should be kept with the S.W.P.P.P. until such time the project is ready for termination of reporting and permit coverage. All records resulting from activities required shall be retained for a period of at least three (3) years from the date of the inspection or report.

## **STAFF TRAINING REQUIREMENTS**

Each operator, or group of multiple operators, must assemble a stormwater team to carry out compliance activities associated with the requirements in this permit. Prior to beginning construction, the personnel on the stormwater team must understand the requirements of this SWPPP and their specific responsibilities.

1. Personnel responsibilities include but are not limited to the following:
2. Personnel who are responsible for the design, installation, maintenance, and/or repair of stormwater controls.
3. Personnel responsible for the application and storage of treatment chemicals, if applicable.
4. Personnel who are responsible for conducting inspections as required and;
5. Personnel who are responsible for taking corrective actions as required.

At a minimum, the stormwater team must be trained to understand applicable procedures to follow with respect to the SWPPP requirements. Each member of the stormwater team must have easy access to an electronic or paper copy of the approved permit, the most updated copy of the SWPPP, and other relative documents or information that must be kept with the SWPPP. Staff training associated with this SWPPP may be documented on

the Employee Training Log provided. Employee training documentation shall be maintained on-site with the SWPPP and made available to MDEQ personnel for inspection upon request.

MDEQ Large Construction Notice of Intent



RECEIVED  
MAY - 6 2026

MDEQ

MISSISSIPPI DEPARTMENT OF  
ENVIRONMENTAL QUALITY

## LARGE CONSTRUCTION NOTICE OF INTENT (LCNOI) FOR COVERAGE UNDER THE LARGE CONSTRUCTION STORM WATER GENERAL NPDES PERMIT

### INSTRUCTIONS

The Large Construction Notice of Intent (LCNOI) is for coverage under the Large Construction General Permit for land disturbing activities of five (5) acres or greater; or for land disturbing activities, which are part of a larger common plan of development or sale that are initially less than five (5) acres but will ultimately disturb five (5) or more acres. Applicant must be the owner or operator. For construction activities, the operator is typically the prime contractor. The owner(s) of the property and the prime contractor associated with regulated construction activity on the property have joint and severable responsibility for compliance with the Large Construction Storm Water General Permit MSR10.

If the company seeking coverage is a corporation, a limited liability company, a partnership, or a business trust, attach proof of its registration with the Mississippi Secretary of State and/or its Certificate of Good Standing. This registration or Certificate of Good Standing must be dated within twelve (12) months of the date of the submittal of this coverage form. Coverage will be issued in the company name as it is registered with the Mississippi Secretary of State.

Completed LCNOIs should be filed at least thirty (30) days prior to the commencement of construction. Discharge of storm water from large construction activities without written notification of coverage is a violation of state law.

Submittals with this LCNOI must include:

- A site-specific Storm Water Pollution Prevention Plan (SWPPP) developed in accordance with ACT5 of the General Permit
- A detailed site-specific scaled drawing showing the property layout and the features outlined in ACT5 of the General Permit
- A United States Geological Survey (USGS) quadrangle map or photocopy, extending at least one-half mile beyond the facility property boundaries with the site location and outfalls outlined or highlighted. The name of the quadrangle map must be shown on all copies. Quadrangle maps can be obtained from the MDEQ, Office of Geology at 601-961-5523.

Additional submittals may include the following, if applicable:

- Appropriate Section 404 documentation from U.S. Army Corps of Engineers
- Appropriate documentation concerning future disposal of sanitary sewage and sewage collection system construction
- Appropriate documentation from the MDEQ Office of Land & Water concerning dam construction and low flow requirements
- Approval from County Utility Authority in Hancock, Harrison, Jackson, Pearl River and Stone Counties
- Antidegradation report for disturbance within Waters of the State

ALL QUESTIONS MUST BE ANSWERED (Answer "NA" if the question is not applicable)

# Best Management Standards

## Construction-Exit Pad (CEP)



### Practice Description

A construction-exit pad is a stone-base pad designed to provide a buffer area where mud- and caked-soil can be removed from the tires of construction vehicles to avoid transporting it onto public roads. This practice applies anywhere traffic will be leaving a construction site and moving directly onto a public road or street.

### Planning Considerations

Roads and streets adjacent to construction sites should be kept clean for the general safety and welfare of the public. A construction-exit pad (Figure CEP-1) should be provided where mud can be removed from construction vehicle tires before they enter a public road.

If the action of the vehicle traveling over the gravel pad does not sufficiently remove the mud, or if the site is in a particularly sensitive area, a washing facility should be included with the pad (Figure CEP-2). When a washing facility is required, all wash water shall be diverted into a sediment trap or basin.

If the construction-exit pad is located in an area with soils that will not support traffic when wet, a geotextile liner located beneath the aggregate will be required to provide stability to the pad.

Construction of stabilized roads throughout the development site should be considered to lessen the amount of mud transported by vehicular traffic. The construction-exit pad

should be located to provide for maximum use by construction vehicles. Consideration should be given to limiting construction vehicles to only one ingress and egress point. Measures may be necessary to make existing traffic use the construction-exit pad.

## Design Criteria and Construction

### Site Preparation

Remove all vegetation and other unsuitable material from the foundation area.

### Grading

Grade and crown the area for positive drainage. Utilize a diversion to direct any surface flow away from the construction-exit pad. Any runoff from the pad should be diverted into a sediment trap or basin. Install a pipe under the pad, if needed, to maintain drainage ditches along public roads.

### Aggregate Size

Aggregate should be Mississippi Department of Transportation Size 1 Stabilizer. Aggregate surface shall be left smooth and sloped for drainage.

### Pad Dimensions

The exit pad shall have a minimum aggregate thickness of 6". The exit pad must be a minimum of 50 feet long and shall provide for entering and parking the longest construction vehicles anticipated. MDOT Drawing ECD-15 provides an example of a stabilized construction entrance. The exit pad shall have a typical width of 20 feet, but may be narrower or wider to equal the full width of the vehicular egress.

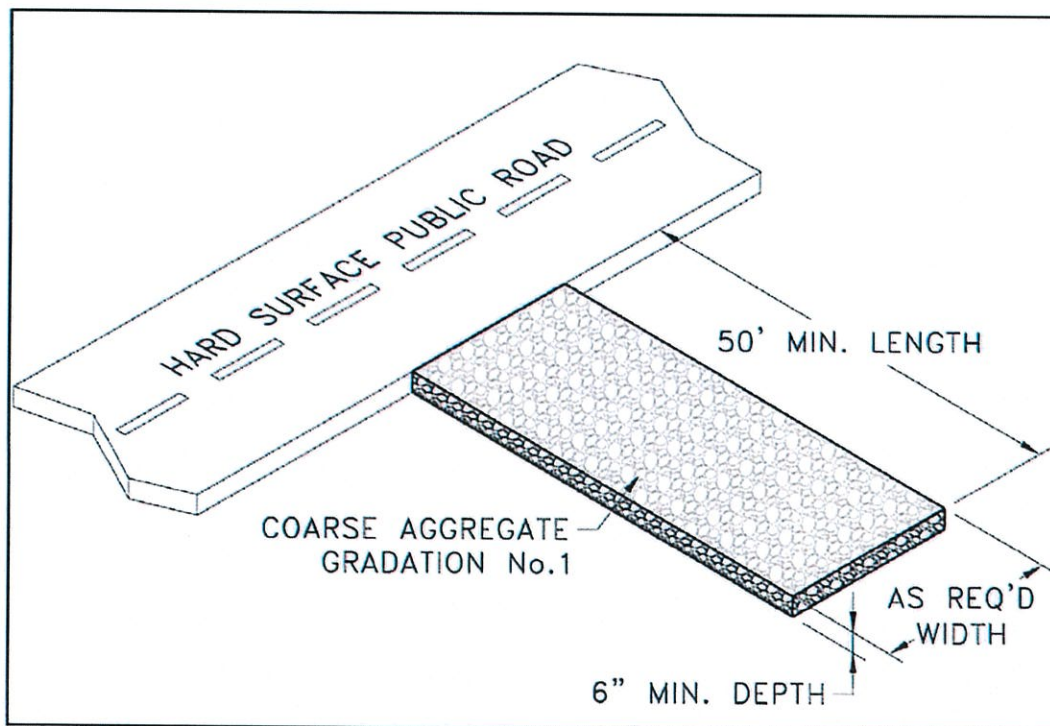


Figure CEP-1 Gravel Construction Exit

**Geotextiles**

A non-woven geotextile meeting the requirements shown in the table below for Class IV geotextiles should be used under the rock when the subgrade is soft or the blow count is less than 10.

Table CEP-1 Requirements for Nonwoven Geotextile

Property	Test method	Class I	Class II	Class III	Class IV <sup>1</sup>
Tensile strength (lb) <sup>2</sup>	ASTM D 4632 grab test	180 minimum	120 minimum	90 minimum	115 minimum
Elongation at failure (%) <sup>2</sup>	ASTM D 4632	≥ 50	≥ 50	≥ 50	≥ 50
Puncture (pounds)	ASTM D 4833	80 minimum	60 minimum	40 minimum	40 minimum
Ultraviolet light (% residual tensile strength)	ASTM D 4355 150-hr exposure	70 minimum	70 minimum	70 minimum	70 minimum
Apparent opening size (AOS)	ASTM D 4751	As specified max. #40 <sup>3</sup>	As specified max. #40 <sup>3</sup>	As specified max. #40 <sup>3</sup>	As specified max. #40 <sup>3</sup>
Permittivity sec <sup>-1</sup>	ASTM D 4491	0.70 minimum	0.70 minimum	0.70 minimum	0.10 minimum

Table copied from NRCS Material Specification 592.

- <sup>1</sup> Heat-bonded or resin-bonded geotextile may be used for classes III and IV. They are particularly well suited to class IV. Needle-punched geotextile required for all other classes.
- <sup>2</sup> Minimum average roll value (weakest principal direction).
- <sup>3</sup> U.S. standard sieve size.

**Washing**

A washing facility shall be provided, if necessary, to prevent mud- and caked-soil from being transported to public streets and highways. It shall be constructed of concrete, stone, and/or other durable materials. Provisions shall be provided for the mud and other material to be carried away from the washing facility into a sediment trap or basin to allow for settlement of the sediment from the runoff before it is released from the site.

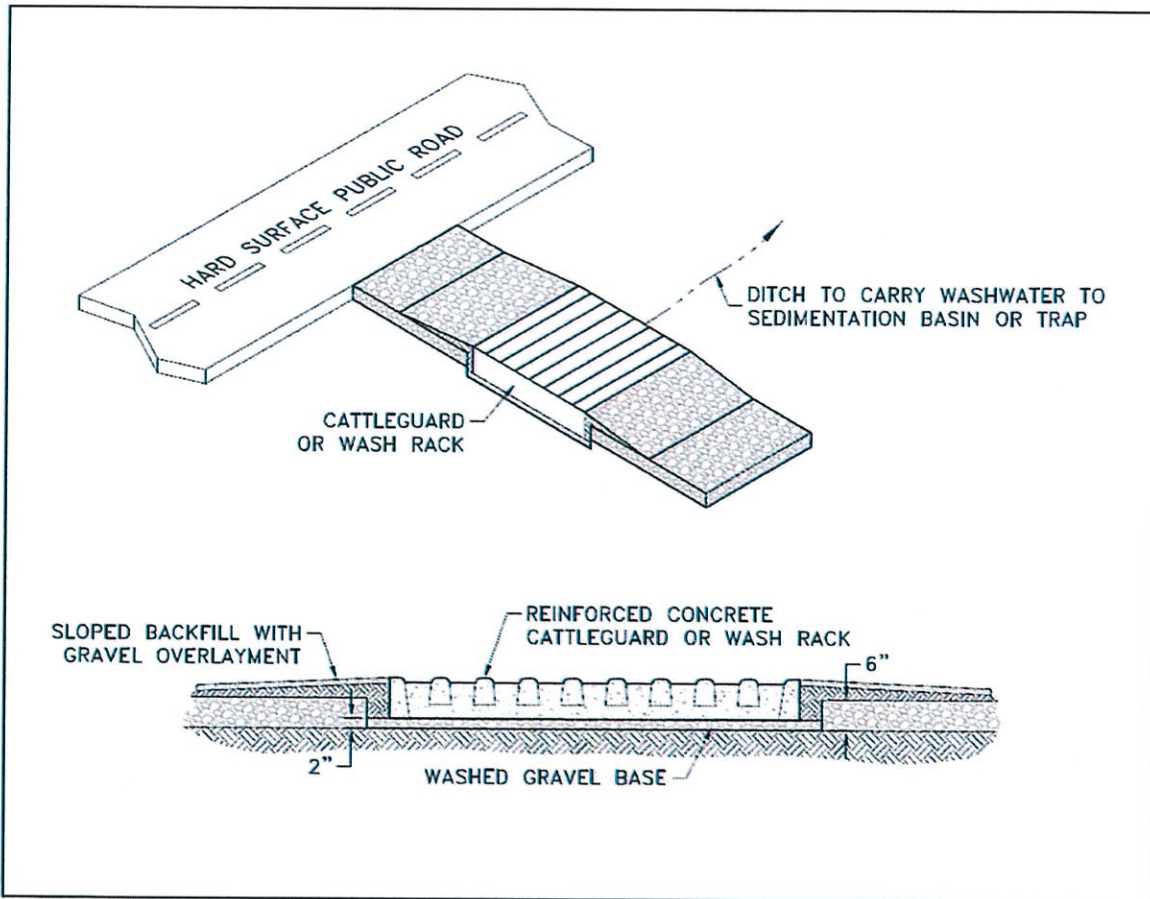


Figure CEP-2 Construction Exit with Wash Rack

## Common Problems

*Consult with a qualified design professional if any of the following occur:*

Inadequate runoff control and sediment washes onto public road: install diversions or other runoff-control measures.

Ruts and muddy conditions develop as stone are pressed into soil: increase stone size or pad thickness, or add geotextile fabric.

Pad too short for heavy-construction traffic: consult design professional about extending pad to the necessary length

## Maintenance

Remove large chunks of mud- or caked-soil from construction-exit pad daily to minimize sediment buildup.

Inspect stone pad and sediment-disposal area weekly and after storm events or heavy use.

Reshape pad as needed for drainage and runoff control.

Top-dress with clean-specified stone as needed to maintain effectiveness of the practice.

Immediately remove mud or sediment tracked or washed onto public road.

Repair any broken-road pavement immediately.

Remove unneeded exit-pad materials from areas where permanent vegetation will be established.

## References

### BMPs from Volume 1


#### Chapter 4

Construction Phasing/Sequencing (CPS)	4-3
Land Grading (LG)	4-16
Housekeeping (HK)	4-43
Preservation of Vegetation (PV)	4-64

### MDOT Drawings Referenced

ECD-15 Stabilized Construction Entrance	4-11
---	------

## Check Dam (CD)



### Practice Description

A check dam is a small barrier or dam constructed across a swale, drainage ditch or other area of concentrated flow for the purpose of reducing channel erosion. Channel erosion is reduced because check dams flatten the gradient of the flow channel and slow the velocity of channel flow. Most check dams are constructed of rock, but hay bales, logs and other materials may be acceptable. Contrary to popular opinion, most check dams trap an insignificant volume of sediment.

This practice applies in small open channels and drainageways, including temporary and permanent swales. It is not to be used in a live stream. Situations of use include areas in need of protection during establishment of grass and areas that cannot receive a temporary or permanent non-erodible lining for an extended period of time.

### Planning Considerations

Check dams are used in concentrated flow areas to provide temporary channel stabilization during the intense runoff periods associated with construction disturbances. Check dams may be constructed of rock, logs, hay bales or other suitable material, including manufactured products. MDOT Drawing ECD-4 at the end of this practice shows the typical application of check dam structures. Most check dams are constructed of rock. Rock may not be acceptable in some installations because of aesthetics; therefore, alternative types of check dams need to be considered.

### Rock check dams

Rock check dams (Figures CD-1 and CD-2) are usually installed with backhoes or other suitable equipment, but hand labor is likely needed to complete most installations to the quality needed. The rock is usually purchased, and some locations in the state may not have rock readily available. The use of rock should be considered carefully in areas to be

mowed. Some rock may be washed away during heavy rain events and should be removed before each mowing operation. Additional installation drawings are provided at the end of this practice as MDOT Drawings ECD-8 and ECD-9.

### Log check dams

Log check dams (Figure CD-3) are more economical from a materials cost standpoint since logs can usually be salvaged from clearing operations. The time and labor required would be greater for log check dams. Increased labor costs would offset the reduced material costs. Log check dams would not be permanent but may last long enough to get grass linings established.

### Hay bale check dams

Check dams constructed of hay bales (Figure CD-4) have the shortest life of the materials discussed and are only used as a temporary means to help establish a channel to vegetation. MDOT Drawing ECD-5 is provided at the end of this practice and shows more specifics for hay bale check dams. MDOT Drawing ECD-6 shows typical details for a straw wattle ditch check as an alternative to hay bale check dams. Hay bale check dams should not be used where permanent watercourse protection is needed and should be used only in concentrated-flow areas where only minimal runoff occurs.

**Without proper installation, which is rarely done, hay bale check dams always fail.**

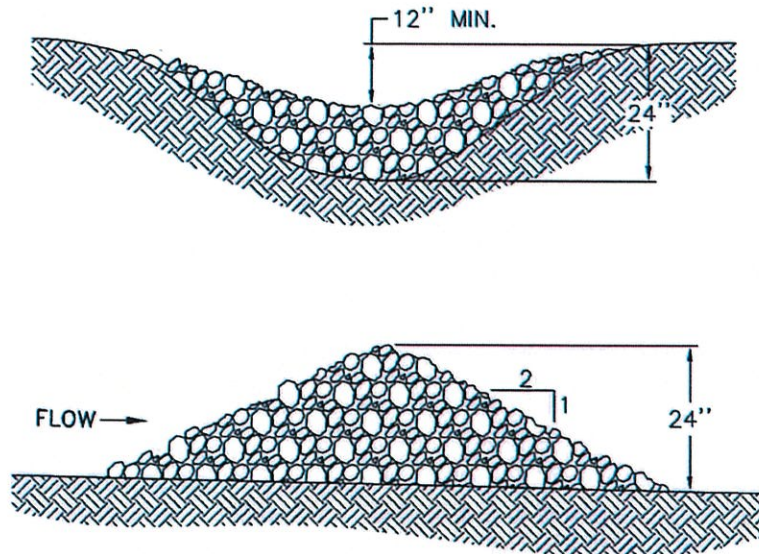


Figure CD-1 Profile of Typical Rock Check Dams

Check dams should be planned to be compatible with the other features such as streets, walks, trails, sediment basins and rights-of-way or property lines. Check dams are normally constructed in series, and the dams should be located at a normal interval from other grade controls such as culverts or sediment basins.

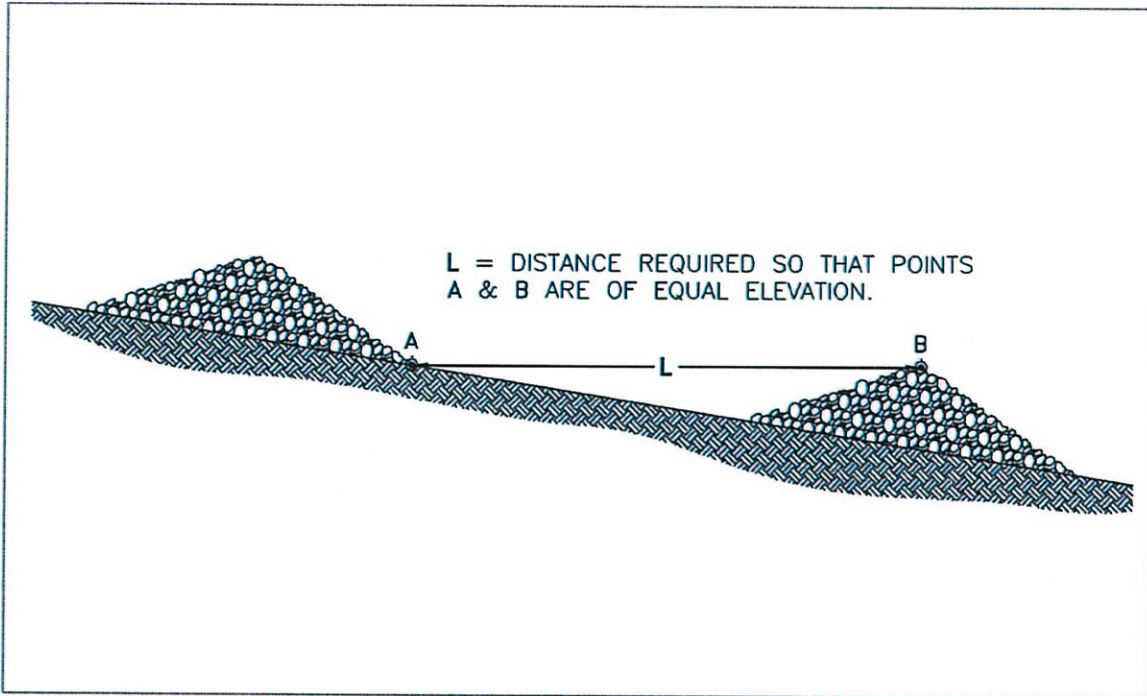


Figure CD-2 Cross Section of Typical Rock Check Dam

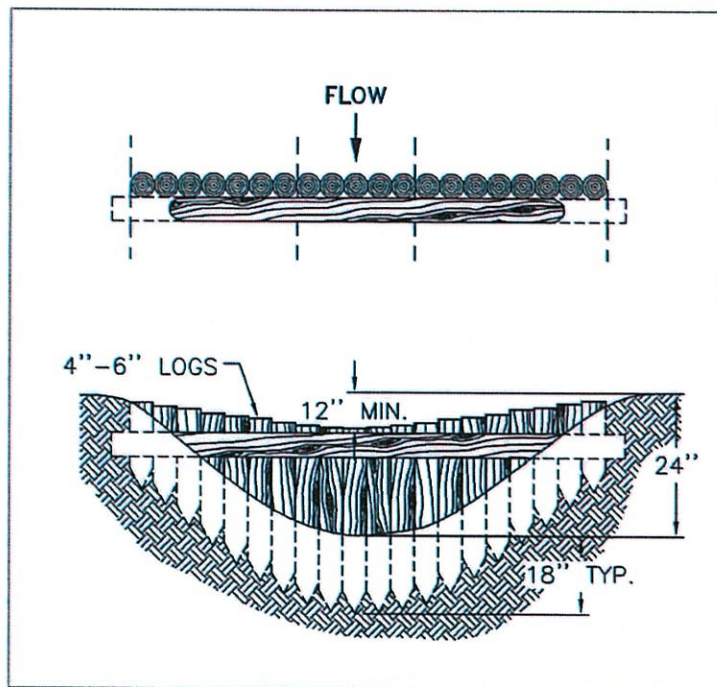


Figure CD-3 Typical Log Check Dam

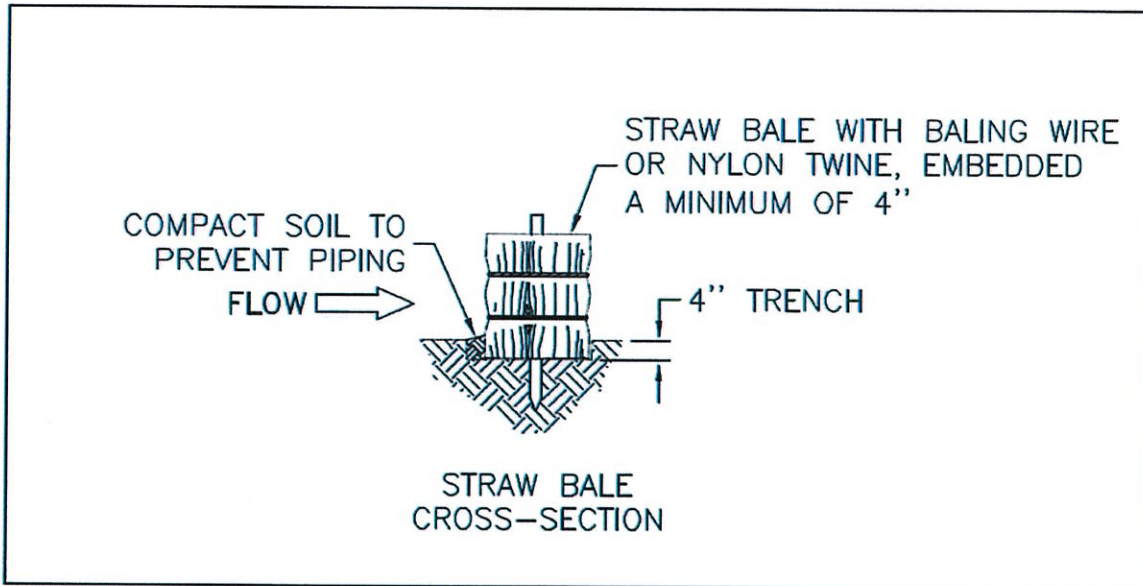


Figure CD-4 Typical Hay Bale Check Dam

(NOTE: Without proper installation, which is rarely done, hay bale check dams always fail.)

### Design Criteria and Installation

Formal design is not required. The following limiting factors should be adhered to when designing check dams.

#### Drainage Area

Ten acres or less (rock or logs).

#### Maximum Height

Two feet when drainage area is less than 5 acres.

Three feet when drainage area is 5 to 10 acres.

#### Depth of Flow

Six inches when drainage area is less than 5 acres.

Twelve inches when drainage area is 5 to 10 acres.

The top of dam, perpendicular to flow, should be parabolic. The center of the dam should be constructed lower than the ends. The elevation of the center of the dam should be lower than the ends by the depth of flow listed above.

#### Side Slopes

2:1 or flatter.

#### Spacing

Elevation of the toe of the upstream dam is at or below elevation of the crest of the downstream dam.

**Keyway**

The rock or log check dam should be keyed into the channel bottom and abutments to a depth of 12 to 24". The keyway width should be at least 12". The keyway is to prevent erosion around the end of and beneath the dam. Hay bale check dams should be embedded into the soil at least 3".

**Rock Check Dams**

Rock check dams should be constructed of durable rock riprap. Rock material diameter should be 2" to 15".

In soils where failure by piping of soils into the rock is likely, a geotextile will be used as a filter to separate the soils from the rock. Geotextile should conform to the requirements of type I geotextile in Table CD-1.

Table CD-1 Requirements for Nonwoven Geotextile

Property	Test method	Class I	Class II	Class III	Class IV <sup>1</sup>
Tensile strength (lb) <sup>2</sup>	ASTM D 4632 grab test	180 minimum	120 minimum	90 minimum	115 minimum
Elongation at failure (%) <sup>2</sup>	ASTM D 4632	≥ 50	≥ 50	≥ 50	≥ 50
Puncture (pounds)	ASTM D 4833	80 minimum	60 minimum	40 minimum	40 minimum
Ultraviolet light (% residual tensile strength)	ASTM D 4355 150-hr exposure	70 minimum	70 minimum	70 minimum	70 minimum
Apparent opening size (AOS)	ASTM D 4751	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>
Permittivity sec <sup>-1</sup>	ASTM D 4491	0.70 minimum	0.70 minimum	0.70 minimum	0.10 minimum

Table copied from NRCS Material Specification 592.

1 Heat-bonded or resin-bonded geotextile may be used for Classes III and IV. They are particularly well suited to Class IV. Needle-punched geotextile is required for all other classes.

2 Minimum average roll value (weakest principal direction).

3 U.S. standard sieve size.

### Site Preparation

Determine location of any underground utilities.

Locate and mark the site for each check dam in strategic locations (to avoid utilities and optimize effectiveness of each structure in flattening channel grade).

Remove debris and other unsuitable material that would interfere with proper placement of the check dam materials.

Excavate a shallow keyway (12"-24" deep and at least 12" wide) across the channel and into each abutment for each check dam.

### Materials Installation

As specified, install a non-woven geotextile fabric in the keyway in sandy or silty soils. This may not be required in clayey soils.

Construct the dam with a minimum 2:1 side slope over the keyway and securely embed the dam into the channel banks. Position rock to form a parabolic top, perpendicular to channel flow, with the center portion at the elevation shown in the design so that the flow goes over the structure and not around the structure.

### Erosion and Sediment Control

Install vegetation (temporary or permanent seeding) or mulching to stabilize other areas disturbed during the construction activities.

### Construction Verification

Check finished size, grade and shape for compliance with standard drawings and materials list (check for compliance with specifications if included in contract specifications).

### Common Problems

*Consult with a qualified design professional if any of the following occur:*

Variations in topography on site indicate check dam will not function as intended. Change in plan will be needed.

Materials specified in the plan are not available.

### Maintenance

Inspect the check dam for rock displacement and abutments for erosion around the ends of the dam after each significant rainfall event. If the rock appears too small, add additional stone and use a larger size.

Inspect the channel after each significant rainfall event. If channel erosion exceeds expectations, consult with the design professional and consider adding another check dam to reduce channel flow grade.

Sediment should be removed if it reaches a depth of ½ the original dam height. If the area behind the dam fills with sediment, there is a greater likelihood that water will flow around the end of the check dam and cause the practice to fail.

Check dams may be removed when their useful life has been completed. The area where check dams are removed should be seeded and mulched immediately unless a different treatment is prescribed. In some instances check dams should be left as a permanent measure to support channel stability.

## References

### BMPs from Volume 1

#### Chapter 4

Temporary Seeding (TS) 4-103

#### MDOT Drawing ECD-4

Ditch Check Structures, Typical Applications and Details 4-124

#### MDOT Drawing ECD-5

Temporary Erosion, Sediment and Water Pollution Control Measures, Silt Fence and Hay Bale Ditch Check 4-125

#### MDOT Drawing ECD-6

Details of Erosion Control Wattle Ditch Check 4-126

#### MDOT Drawing ECD-7

Details of Erosion Control Silt Dike Ditch Check 4-127

#### MDOT Drawing ECD-8

Rock Ditch Check 4-128

#### MDOT Drawing ECD-9

Rock Ditch Check with Sump Excavation 4-129

#### MDOT Drawing ECD-20

Details of Erosion Control Sandbag Ditch Check 4-130

## Sediment Barrier (SB)

SILT FENCE   
STRAW BALE BARRIER 



### Practice Description

Silt fencing is a temporary sediment barrier used across a landscape to reduce the quantity of sediment that is moving farther downslope. Commonly used barriers include silt fence (a geotextile fabric that is trenched into the ground and attached to supporting posts) or hay bales trenched into the ground. Other barrier materials include sand bags, brush piles, and various man-made materials and devices that can be used in a similar manner as silt fence and hay bales.

This practice applies where sheet and rill erosion occurs on small disturbed areas. Barriers intercept runoff from upslope to form ponds that temporarily store runoff and allow sediment to settle out of the water and stay on the construction site.

### Planning Considerations

Sediment barriers may be used on developing sites. They should be installed on the contour so that flow will not concentrate and cause bypassing by runoff going around the end of the barrier or overtopping because of lack of storage capacity.

The most commonly used sediment barriers are silt fences, manufactured sediment logs (several names other than “logs” are used), and hay bales. Silt fences and manufactured sediment logs are preferable to hay bales because they are more likely to be installed correctly. The design and installation of a hay bale sediment barrier is the same as for *Straw Bale Sediment Traps*. Manufactured sediment logs should be installed according to manufacturer’s recommendations.

The silt fence is the only sediment barrier covered in this manual.

The success of silt fences depends on a proper installation that causes the fence to develop maximum efficiency of sediment trapping. Silt fences should be carefully installed to meet the intended purpose.

A silt fence is specifically designed to retain sediment transported by sheet flow from disturbed areas, while allowing water to pass through the fence. Silt fences should be installed to be stable under the flows expected from the site. Silt fences should not be installed across streams, ditches, waterways, or other concentrated flow areas.

Silt fences are composed of woven geotextile supported between steel or wooden posts. Silt fences are commercially available with geotextile attached to the post, and can be rolled out and installed by driving the post into the ground. This type of silt fence is simple to install, but more expensive than some other installations. Silt fences must be trenched in at the bottom to prevent runoff from undermining the fence and developing rills under the fence. Locations with high runoff flows or velocities should use wire reinforcement.

### Design Criteria

Silt fence installations are normally limited to situations in which only sheet- or overland-flow is expected because they normally cannot pass the volumes of water generated by channel flows. Silt fences are normally constructed of synthetic fabric (woven geotextile), and the life is expected to be the duration of most construction projects. Silt fence fabric should conform to the requirements of Table SB-1.

The drainage area behind the silt fence should not exceed  $\frac{1}{4}$  acre per 100 linear feet of silt fence for non-reinforced fence and  $\frac{1}{2}$  acre per 100 linear feet of wire-reinforced fence. When all runoff from the drainage area is to be stored behind the fence (i.e. no stormwater disposal system is in place), the maximum slope length behind the fence should not exceed the value shown in Table SB-2.

### Type A Silt Fence

The Type A fence is 36" wide with wire reinforcement and is used on sites needing the highest degree of protection by a silt fence. The wire reinforcement is necessary because the Type A silt fence is used for the highest flow situations and has almost 3 times the flow rate as the Type B silt fence. Type A silt fence should be used where runoff flows or velocities are particularly high or where slopes exceed a vertical height of 10 feet.

Provide a riprap splash pad or other outlet protection device for any point where flow may overtop the sediment fence. Ensure that the maximum height of the fence at a protected, reinforced outlet does not exceed 1 foot and that support post spacing does not exceed 4 feet.

This silt fence should be installed as shown in Figure SB-1. Materials for posts and fasteners are shown in Tables SB-3 and SB-4. Details for overlap of the silt fence and fastener placement are shown in Figure SB-4.

Table SB-1 Specifications for Silt Fence

Specifications	Type A	Type B	Type C
Tensile Strength (Lbs. Min.) <sup>1</sup> (ASTM D-4632)	Warp – 260 Fill – 100	Warp – 120 Fill – 100	Warp – 120 Fill – 100
Elongation (% Max.) (ASTM D-4632)	40	40	40
AOS (Apparent Opening Size) (Max. Sieve Size) (ASTM D-4751)	No. 30	No. 30	No. 30
Flow Rate (Gal/Min/Sq. Ft.) (GDT-87)	70	25	25
Ultraviolet Stability <sup>2</sup> (ASTM D-4632 after 300 hours weathering in accordance with ASTM D-4355)	80	80	80
Bursting Strength (PSI Min.) (ASTM D-3786 Diaphragm Bursting Strength Tester)	175	175	175
Minimum Fabric Width (Inches)	36	36	22

<sup>1</sup> Minimum roll average of five specimens.

<sup>2</sup> Percent of required initial minimum tensile strength.

Table SB-2 Slope Limitations for Silt Fence

Land Slope (Percent)	Maximum Slope Length Above Fence (Feet)
<2	100
2 to 5	75
5 to 10	50
10 to 20*	25
>20	15

\*In areas where the slope is greater than 10%, a flat area length of 10 feet between the toe of the slope to the fence should be provided.

### Type B Silt Fence

This 36" wide filter fabric should be used on developments where the life of the project is greater than or equal to 6 months.

This silt fence should be installed as shown in Figure SB-2. Materials for posts and fasteners are shown in Tables SB-3 and SB-4. Details for overlap of the silt fence and fastener placement are shown in Figure SB-4.

### Type C Silt Fence

Though only 22" wide, this filter fabric allows the same flow rate as Type B silt fence. Type C silt fence should be limited to use on relatively minor projects, such as residential

home sites or small commercial developments where permanent stabilization will be achieved in less than 6 months.

This silt fence should be installed as shown in Figure SB-3. Materials for posts and fasteners are shown in Tables SB-3 and SB-4. Details for overlap of the silt fence and fastener placement are shown in Figure SB-4.

Table SB-3 Post Size for Silt Fence

	Minimum Length	Type of Post	Size of Post
<b>Type A</b>	4'	Steel	1.3 lb./ft. min.
<b>Type B</b>	4'	Soft Wood	3" diameter or 2 X 4
		Oak	1.5" X 1.5"
		Steel	1.3 lb./ft. min.
<b>Type C</b>	3'	Soft Wood	2" diameter or 2 X 2
		Oak	1" X 1"
		Steel	0.75 lb./ft. min.

Table SB-4 Wood Post Fasteners for Silt Fence

	Gauge	Crown	Legs	Staples/Post
<b>Wire Staples</b>	17 min.	¾" wide	½" long	5 min.
	Gauge	Length	Button Heads	Nail/Post
<b>Nails</b>	14 min.	1"	¾" long	4 min.

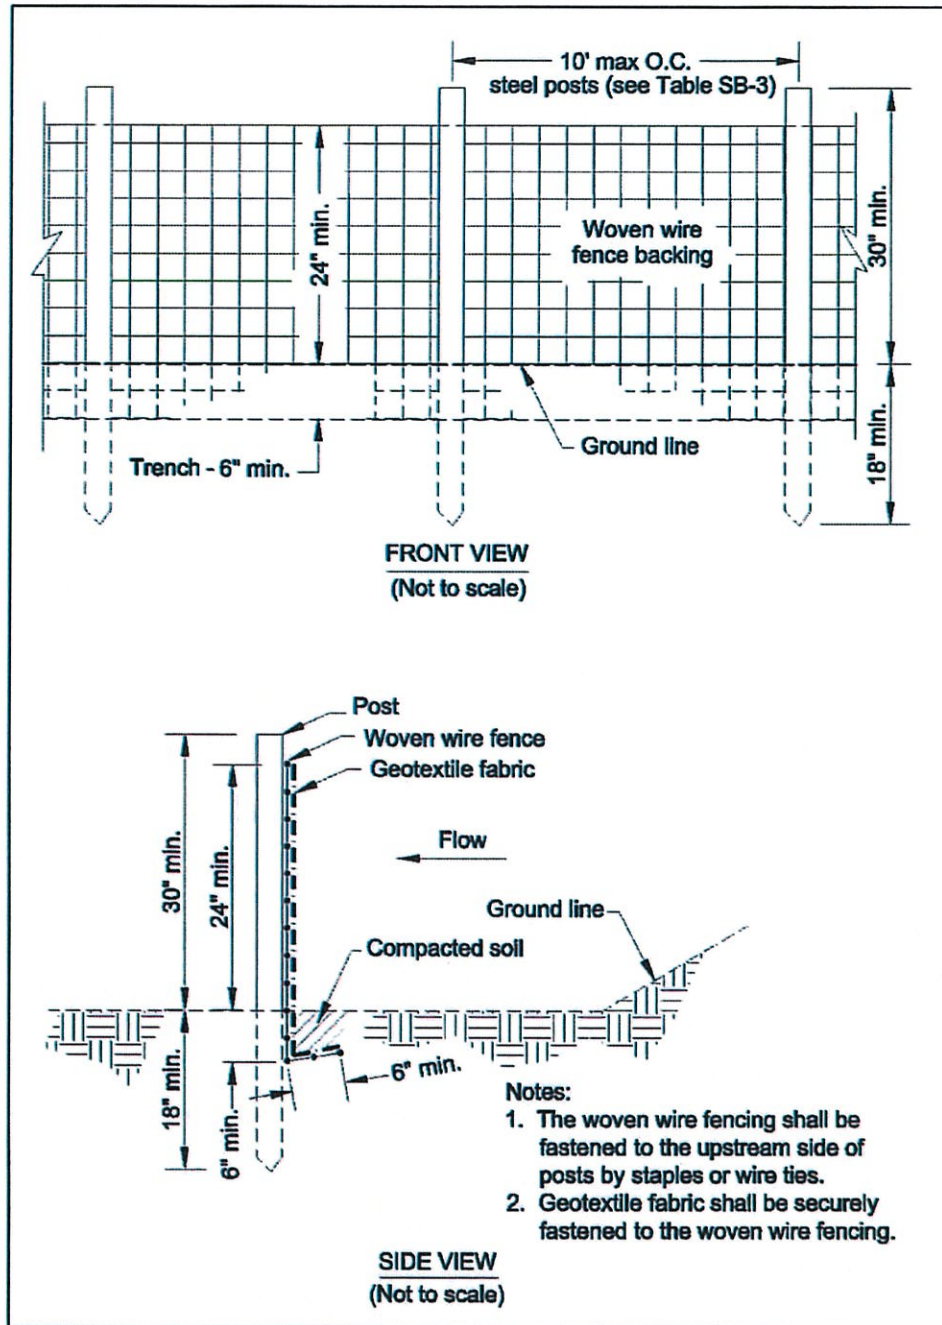


Figure SB-1 Silt Fence-Type A

- (1) For fabric material requirements see Table SB-1
- (2) For post material requirements see Tables SB-3 and SB-4

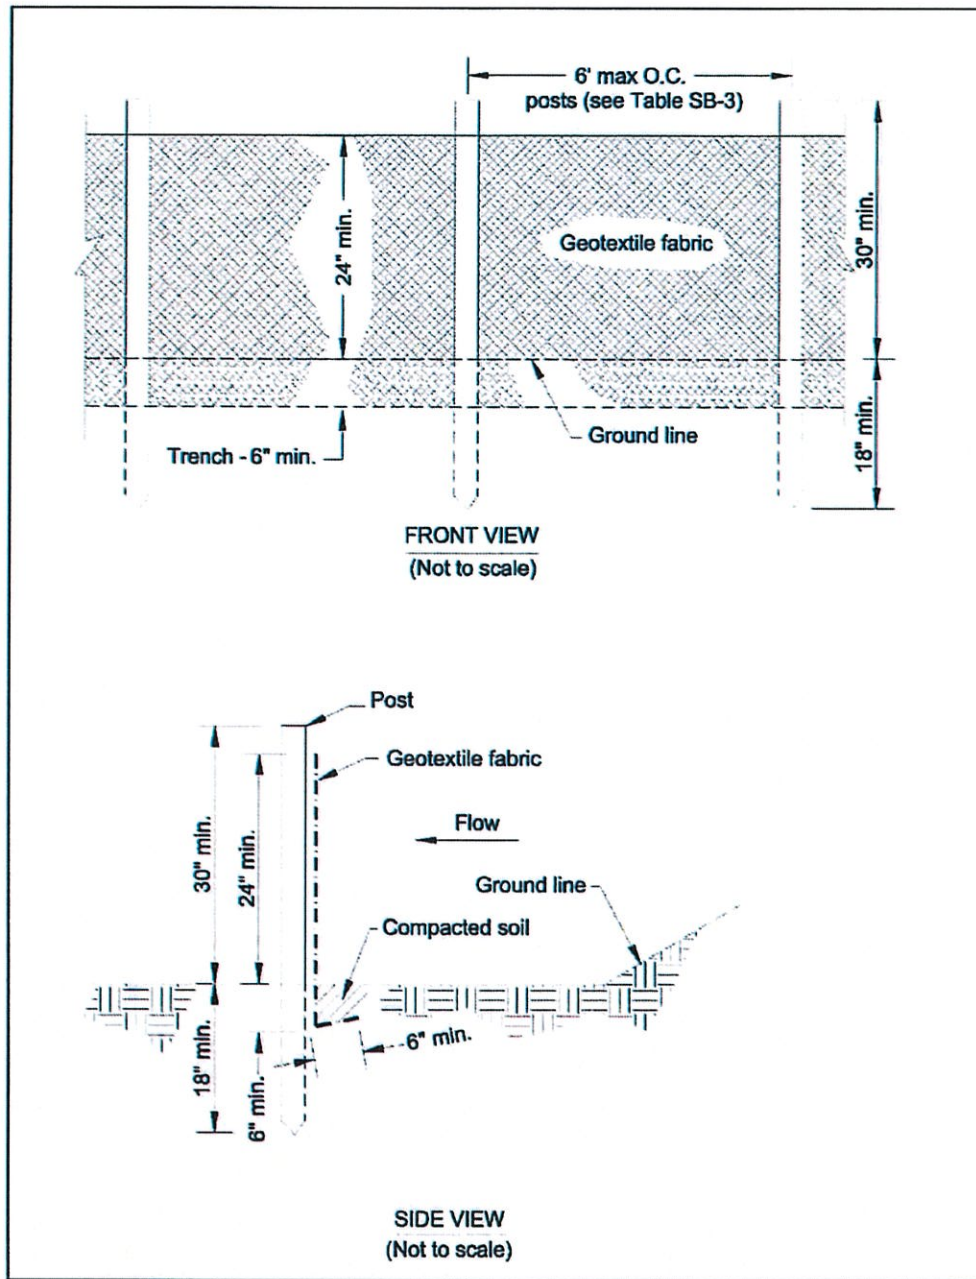


Figure SB-2 Silt Fence - Type B

- (1) For fabric material requirements see Table SB-1
- (2) For post material requirements see Tables SB-3 and SB-4

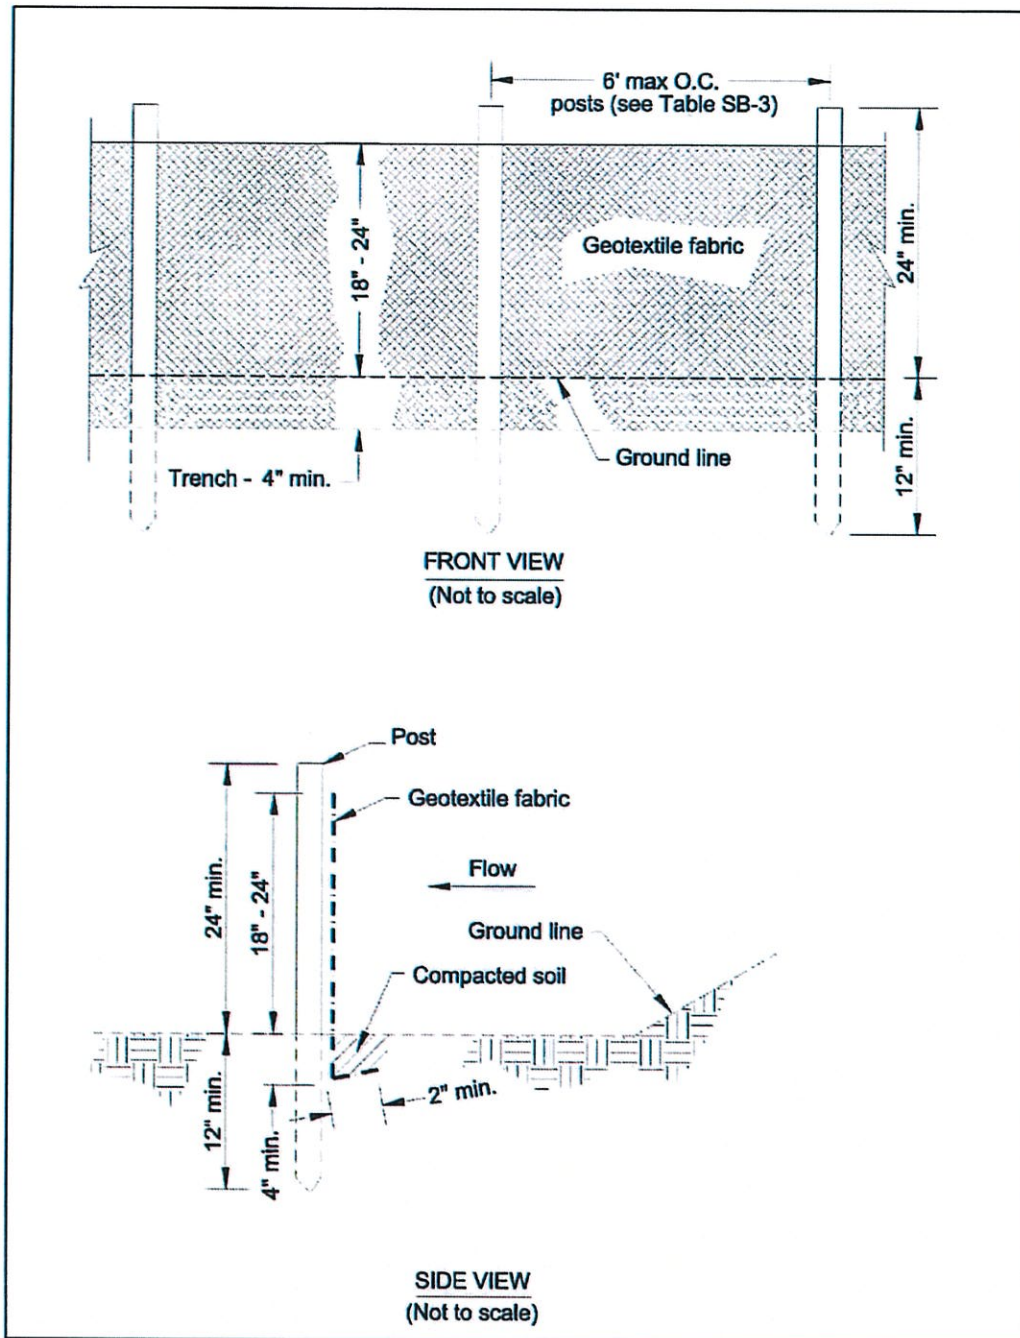


Figure SB-3 Silt Fence – Type C

- (1) For fabric material requirements see Table SB-1
- (2) For post material requirements see Tables SB-3 and SB-4

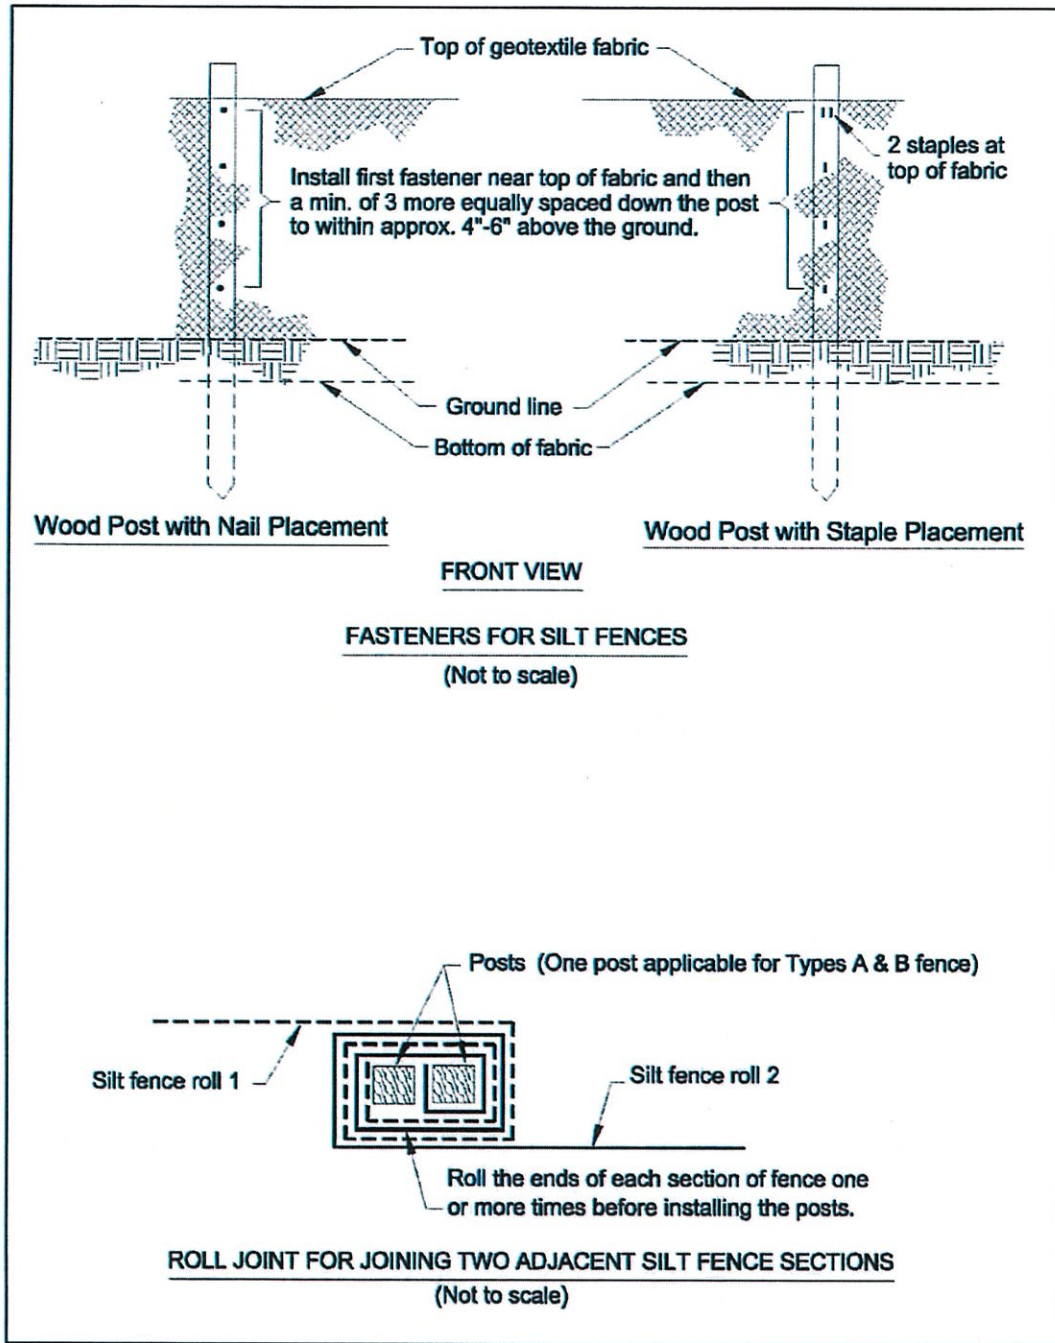


Figure SB-4 Silt Fence Installation Details

## Construction

Prior to start of construction, sediment barriers should be designed by a qualified professional. Plans and specifications should be referred to by field personnel throughout the construction process.

*Note: Silt fence is the only barrier installation being covered in this handbook.*

## Site Preparation

Determine exact location of underground utilities so that locations for digging or placement of stakes can be selected where utilities will not be damaged.

Smooth the construction zone to provide a broad, nearly level area for the fence. The area should be wide enough throughout the length of the fence to provide storage of runoff and sediment behind the fence.

## Silt Fence Installation

Silt fence should be installed on the contour, so that runoff can be intercepted as sheet flow; ends should be flared uphill to provide temporary storage of water. Silt fence should be placed so that runoff from disturbed areas must pass through the fence. Silt fence should not be placed across concentrated flow areas such as channels or waterways. When placed near the toe of a slope, the fence should be installed far enough from the slope toe to provide a broad, flat area for adequate storage capacity for sediment. Dig a trench at least 6" deep along the fence alignment as shown in Figures SB-1 and SB-2 for Types A & B fences. Type C fences require only a 4" deep trench as shown in Figure SB-3. **Please note that installation with a silt fence installation machine may permit different depths if performance is equal.**

Drive posts at least 18" into the ground on the downslope side of the trench. Space posts a maximum of 10 feet if fence is supported by woven wire, or 6 feet if high-strength fabric and no support fence is used.

Fasten support wire fence to upslope side of posts, extending 6" into the trench, as shown in the appropriate figure for the type fence (see Figure SB-1, SB-2 or SB-3).

Attach a continuous length of fabric to the upslope side of fence posts. Minimize the number of joints and, when necessary to join rolls, they should be joined by rolling the ends together using the "roll joint" method illustrated in Figure SB-4. Avoid joints at low points in the fence line.



For Types A and B silt fence, place the bottom 12" of fabric in the 6" deep (minimum) trench, lapping toward the upslope side. For Type C fabric, place the bottom 6" in the 4" deep (minimum) trench lapping toward the upslope side.

Backfill the trench with compacted earth or gravel as shown in Figures SB-1 – SB-3.

Provide good access in areas of heavy sedimentation for cleanout and maintenance.

### **Erosion Control**

Stabilize disturbed areas in accordance with the vegetation plan. If no vegetation plan exists, consider planting and mulching as a part of barrier installation, and select planting information from the appropriate planting practice (*Permanent Seeding* or *Temporary Seeding*). Select mulching information from the *Mulching Practice*.

### **Construction Verification**

Check finished grades and dimensions of the sediment fence. Check materials for compliance with specifications.

### **Common Problems**

*Consult with a qualified design professional if any of the following occurs:*

Variations in topography on site indicate sediment fence will not function as intended, or alignment is not on contour, or fence crosses concentrated flow areas; changes in plan may be needed.

Design specifications for filter fabric, support posts, support fence, gravel, or riprap cannot be met; substitutions may be required. Unapproved substitutions could lead to failure.

Drainage area appears to exceed ¼ acre for 100 feet of non-reinforced silt fence and ½ acre for 100 feet for reinforced fence. Additional sediment-control BMPs may be required.

### **Maintenance**

Inspect sediment fences at least once a week and after each significant rain event.

Make required repairs immediately.

Should the fabric of silt fence collapse, tear, decompose, or become ineffective, replace it promptly.

Remove sediment deposits when they reach a depth of 15" or ½ the height of the fence as installed, to provide adequate storage volume for the next rain event and to reduce pressure on the fence.

After the contributing drainage area has been properly stabilized, remove all barrier materials and unstable sediment deposits, bring the area to grade, and stabilize it with vegetation.

## References

### BMPs from Volume I

#### Chapter 4

Mulching (MU) 4-48

### MDOT Drawing ECD-2

Details of Sediment Barrier Applications 4-295


### MDOT Drawing ECD-3

Details of Silt Fence Installation 4-296

### MDOT Drawing SSF-1

Super Silt Fence 4-297

## Fabric Drop Inlet Protection (FIP)

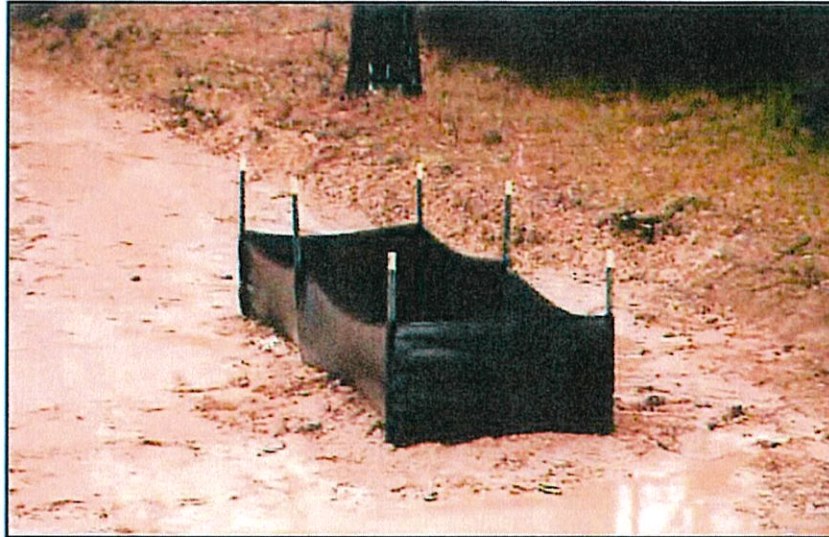

### Practice Description

Fabric drop inlet protection is a structurally supported geotextile barrier placed around or over a drop inlet to prevent sediment from entering storm drains during construction. This practice applies where early use of the storm drain system is necessary prior to stabilization of the disturbed drainage area. This practice is suitable for inlets with a drainage area of less than 1 acre and a gentle approach slope generally of 1% or less.

### Planning Considerations

Storm sewers that are made operational before their drainage area is stabilized can convey large amounts of sediment to natural drainage ways. In case of extreme sediment loading, the storm sewer itself may clog and lose a major portion of its capacity. To avoid these problems, it is necessary to prevent sediment from entering the system at the inlets that discharge directly to waters of the state.

The best way to prevent sediment from entering the storm sewer system is to stabilize the site as quickly as possible, preventing erosion and stopping sediment at its source. Sediment is best treated by preventing erosion. Leave as much of the site undisturbed as possible in the total site plan. Clear and disturb the site in small increments, if possible.

Numerous products have been developed to facilitate the capture of suspended soil particles at inlets. The design criteria for performance should be considered when evaluating alternative products. Products that will likely not meet performance goals or that usually fail under storm conditions should not be selected.

## Design Criteria and Installation

Prior to start of construction, fabric drop inlet protection structures should be designed by a qualified professional. Plans and specifications should be available to field personnel. (*Note: Premanufactured fabric drop inlet protective structures should be installed and maintained according to the manufacturer's requirements.*)



### Drainage Area

Drainage area should be less than 1 acre per inlet.

### Sediment Storage

The basin created at the inlet should provide 67 cubic yards per disturbed acre of sediment storage.

### Site Preparation

The soil around the drop inlet should be well compacted. The area around the drop inlet should be shaped, if necessary, to store the runoff on an almost level area. If runoff could bypass the protected inlet, a temporary dike should be planned and force the runoff to be trapped by the protective device.

### Approach

The approach to the inlet protection practice should generally be less than 1% slope.

### Height

The height of the structurally supported geotextile should be at least 1 foot but no more than 2.5 feet. The base of the fabric should be buried with compacted earth fill at least 12 inches into the soil or extend horizontally and be adequately secured with ballast material according to the manufacturer's recommendations. Ensure that the height of the structure when fully ponded does not cause unintentional damage or hazards to adjacent areas.

### Structural Frame Installation

The frame (premanufactured or constructed) should provide the internal support necessary to prevent the structure from buckling, the fabric from sagging, or the fabric from being undermined. Frames should be positioned so that water that overtops the device goes directly into the inlet and does not cause erosion between the frame and inlet. Premanufactured frames should be installed according to manufacturer's recommendations.

### Fabric Installation

Generally, fabric is installed by one of two methods:

Fabric can be buried vertically in a trench. The trench is excavated at least 12 inches into compacted soil adjacent to the inlet. Support posts are installed securely against the exterior of the drop inlet. Fabric along with wire fence is secured in the bottom of the trench and against the exterior surface of the inlet with stakes no more than 2 feet apart

and driven at least 6 inches into the soil. The trench is backfilled with hand-compacted soil to the density equivalent to the surrounding soil. Fence and fabric are secured to the posts and the structure internally supported to meet the structural requirements of the device.

Fabric for pre-manufactured drop inlet protective devices is generally secured with ballast pockets on well-compacted soil around the inlet. Install these according to manufacturer's recommendations

### **Performance**

Either the system of protection for the project or the drop inlet protection that discharges directly to the outfall of the project must be designed to meet the NTU requirements for discharge.

### **Stabilization**

Stabilize all bare areas that drain to the inlet with temporary seeding and mulching unless construction will disturb it within 13 days.

### **Safety**

Protection should be provided to prevent children from entering open-top structures.

### **Construction Verification**

Check finished grades and dimensions of fabric drop inlet protection structures.

### **Common Problems**

*Consult with a qualified design professional if any of the following occurs:*

Variations in site conditions indicate that the practice will not function as intended; change in plan may be needed.

Sediment not removed from pool resulting in inadequate storage volume for the next storm.

Top of fabric set too high, resulting in flow bypassing the inlet.

Fabric is not adjacent to the inlet exterior surface, resulting in erosion and undercutting of inlet.

### **Maintenance**

Inspect fabric barrier after each rainfall event and make needed repairs immediately.

Remove sediment from the pool area when sediment has reached ½ the fabric height. Take care not to damage or undercut the fabric during the sediment removal.

When the contributing drainage area has been adequately stabilized, remove all materials and unstable sediment and dispose of properly. Fill the disturbed area to the grade of the drop inlet. Stabilize disturbed areas in accordance with the plans.

## References

### BMPs from Volume 1

#### Chapter 4

Sediment Barrier (SB)	4-284
Sediment Basin (SBN)	4-298

### MDOT Drawing ECD-3

Details of Silt Fence Installation	4-247
------------------------------------	-------

### MDOT Drawing ECD-13

Inlet Protection Details of Manufactured Inlet Protection	4-248
---	-------

## Temporary Seeding (TS)

TS



### Practice Description

Temporary seeding is the establishment of fast-growing annual vegetation from seed on disturbed areas. Temporary vegetation provides economical erosion control for up to a year and reduces the amount of sediment moving off the site.

This practice applies where short-lived vegetation can be established before final grading or in a season not suitable for planting the desired permanent species. It helps prevent costly maintenance operations on other practices such as sediment basins and sediment barriers. In addition, it reduces problems of mud and dust production from bare soil surfaces during construction. Temporary or permanent seeding is necessary to protect earthen structures such as dikes, diversions, grass-lined channels and the banks and dams of sediment basins.

### Planning Considerations

Temporary vegetative cover can provide significant short-term erosion and sediment reduction before establishing perennial vegetation.

Temporary vegetation will reduce the amount of maintenance associated with sediment basins.

Temporary vegetation is used to provide cover for no more than 1 year. Permanent vegetation should be established at the proper planting time for permanent vegetative cover.

Certain plants species used for temporary vegetation will produce large quantities of residue which can provide mulch for establishment of the permanent vegetation.

Proper seedbed preparation and selection of appropriate species are important with this practice. Failure to follow establishment guidelines and recommendations carefully may result in an inadequate or short-lived stand of vegetation that will not control erosion.

The selection of plants for temporary vegetation must be site specific. Factors that should be considered are types of soils, climate, establishment rates, and management requirements of the vegetation. Other factors that may be important are wear, mowing tolerance, and salt tolerance of vegetation.

Seeding properly carried out within the optimum dates has a higher probability of success. It is also possible to have satisfactory establishment when seeding outside these dates. However, as plantings are deviated from the optimum dates, the probability of failure increases rapidly. Seeding dates should be taken into account in scheduling land-disturbing activities.

Site quality impacts both short-term and long-term plant success. Sites that have compacted soils should be modified whenever practical to improve the potential for plant growth.

The operation of equipment is restricted on slopes steeper than 3:1, severely limiting the quality of the seedbed that can be prepared. Provisions for establishment of vegetation on steep slopes can be made during final grading. In construction of fill slopes, for example, the last 4-6" might not be compacted. A loose, rough seedbed with irregularities that hold seeds and fertilizer is essential for hydroseeding. Cut slopes should be roughened (see practice *Land Grading*).

Good mulching practices are critical to protect against erosion on steep slopes. When using straw, anchor with netting or asphalt. On slopes steeper than 2:1, jute, excelsior, or synthetic matting may be required to protect the slope.

The use of irrigation (temporary or permanent) will greatly improve the success of vegetation establishment.

### **Design Criteria and Installation**

Prior to start of installation, plant materials, seeding rates and planting dates should be specified by a qualified design professional. Plans and specifications should be referred to by field personnel throughout the installation process.

### **Scheduling**

Plantings should be made during the specified planting period if possible. When sites become available to plant outside of the recommended planting period, either temporary seeding, mulching or chemical stabilization will be more appropriate than leaving the surface bare for an extended period. If lime and fertilizer application rates are not specified, take soil samples during the final grading operation from the top 6" in each area to be seeded. Submit samples to a soil testing laboratory for lime and fertilizer recommendations.

**Plant Selection**

Select plants that can be expected to meet planting objectives. To simplify plant selection, use Table TS-1, *Commonly Used Plants for Temporary Cover* and Figure TS-1, *Geographical Areas for Species Adaptation and Seeding Dates*. Seeding mixtures commonly specified by the Mississippi Department of Transportation are an appropriate alternative for plantings on rights-of-ways. Additional information related to plantings in Mississippi is found in Chapter 2 in the section *Non-woody Vegetation for Erosion and Sediment Control*.

Table TS-1 Commonly Used Plants for Temporary Cover

Species	Seeding Rates/Ac	Planting Time	Desired pH Range	Fertilization Rate/Acre	Method of Establishment	Zone of Adaptability
Wheat	90 lbs. alone	9/1 – 11/30	6.0 – 7.0	600 lbs. 13-13-13	Seed	All
Ryegrass	30 lbs.	9/1 – 11/30	6.0 – 7.0	600 lbs. 13-13-13	Seed	All
White Clover	5 lbs	9/1 – 11/30	6.0 – 7.0	400 lbs. 13-13-13	Seed	All
Crimson Clover	25 lbs. alone 15 lbs. mix	9/1 – 11/30	6.0 – 7.0	400 lbs. 13-13-13	Seed	All
Hairy Vetch	30 lbs.	9/1 – 11/30	6.0 – 7.0	400 lbs. 13-13-13	Seed	All
Browntop Millet	40 lbs. alone 15 lbs. mix	4/1 – 8/30	6.0 – 7.0	600 lbs. 13-13-13	Seed	All

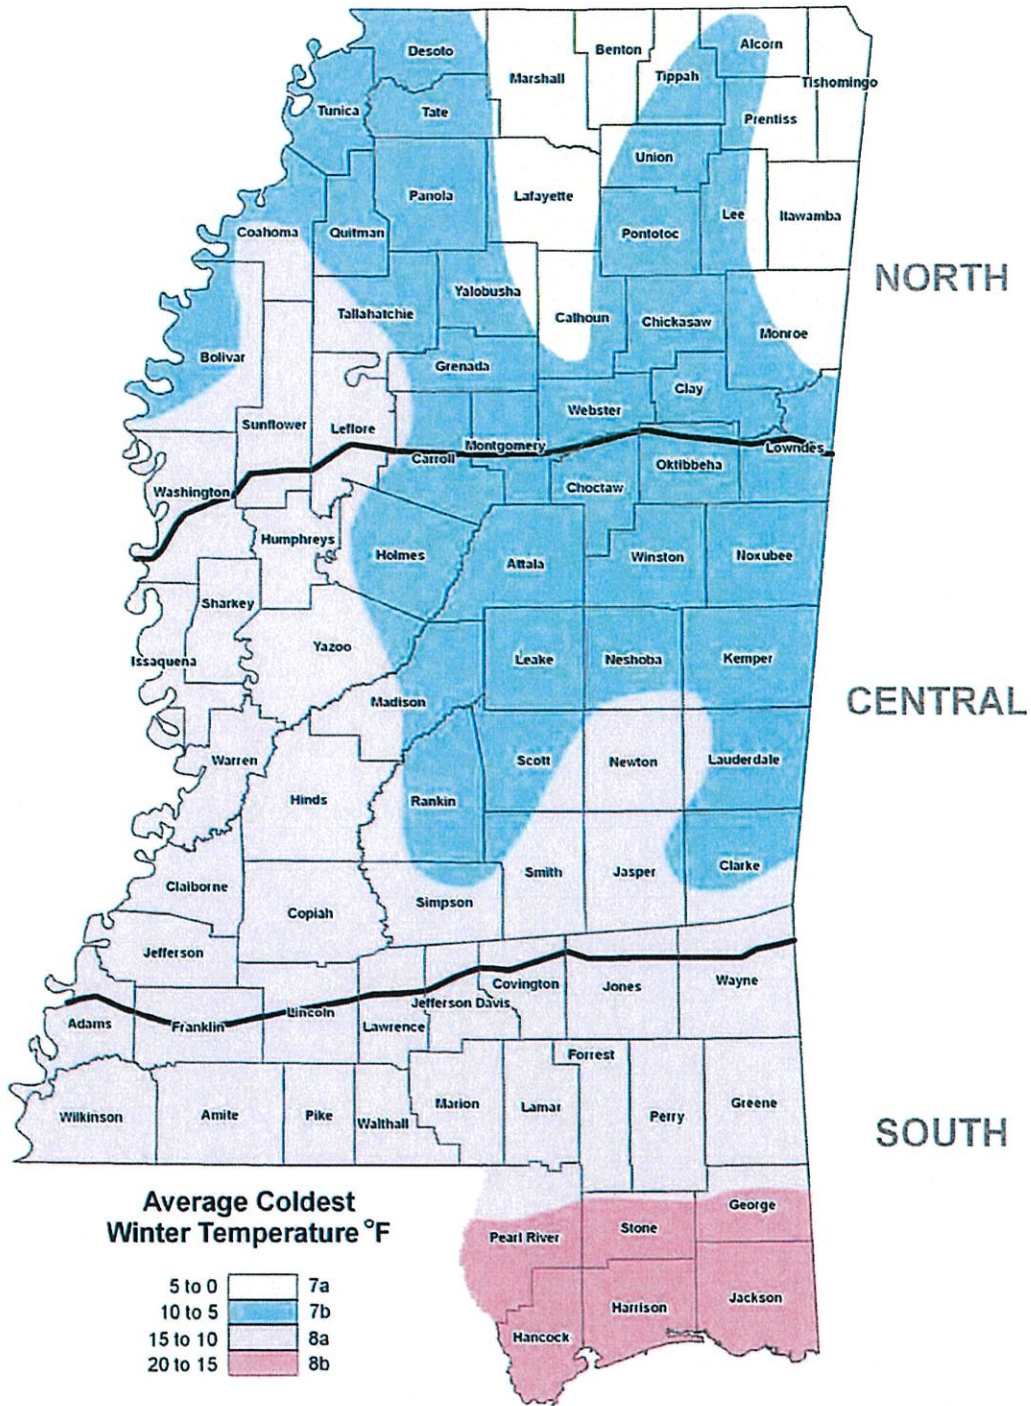


Figure TS- 1 Geographical Areas for Species Adaptation

### **Site Preparation and Soil Amendments**

Complete grading and shaping before applying soil amendments, if needed, to provide a surface on which equipment can safely and efficiently be used to apply soil amendments and accomplish seedbed preparation and seeding. Incorporate lime and fertilizer into the top 6" of soil during seedbed preparation.

#### **Lime**

Apply lime according to soil-test recommendations. If a soil test is not available, use 1 ton of agricultural limestone or equivalent per acre on coarse-textured soils and 2 tons per acre on fine textured soils. Do not apply lime to alkaline soils or to areas that have been limed during the preceding 2 years. Other liming materials that may be selected should be provided in amounts that provide equal value to the criteria listed for agricultural lime or be used in combination with agricultural limestone or Selma chalk to provide equivalent values to agricultural limestone.

#### **Fertilizer**

Apply fertilizer according to soil-test results. If a soil test is not available, apply 8-24-24 fertilizer.

When vegetation has emerged in a stand and is growing, 30 to 40 lbs/acre (approximately 0.8 lbs/1000 ft<sup>2</sup>) of additional nitrogen fertilizer should be applied.

*Note: Fertilizer can be blended to meet exact fertilizer recommendations. Take soil-test recommendations to local fertilizer dealer for bulk-fertilizer blends. This may be more economical than bagged fertilizer.*

### **Seedbed Preparation**

Good seedbed preparation is essential to successful plant establishment. A good seedbed is well pulverized, loose, and smooth. If soils become compacted during grading, loosen them to a depth of 6" to 8" using a ripper or chisel plow.

If rainfall has caused the surface to become sealed or crusted, loosen it just prior to seeding by disking, raking, harrowing, or other suitable methods. When hydroseeding methods are used, the surface should be left with a more irregular surface of clods.

### **Planting Methods**

#### **Seeding**

Evenly apply seed using a cyclone seeder (broadcast), drill seeder, cultipacker seeder, or hydroseeder. Broadcast seeding and hydroseeding are appropriate for steep slopes where equipment cannot operate safely. Small grains should be planted no more than 1" deep, and grasses and legumes no more than ½" deep. Seed that are broadcast must be covered by raking or chain dragging, and then lightly firmed with a roller or cultipacker.

#### **Hydroseeding**

Surface roughening is particularly important when hydroseeding, as a roughened slope will provide some natural coverage for lime, fertilizer, and seed. The surface should not be compacted or left smooth. Fine seedbed preparation is not necessary

for hydroseeding operations; large clods, stones, and irregularities provide cavities in which seeds can lodge.

Mix seed, use an inoculant if required, and mix a seed carrier with water and apply as slurry uniformly over the area to be treated. The seed carrier should be a cellulose fiber, natural-wood fiber or other approved fiber-mulch material which is dyed an appropriate color to facilitate uniform application of seed. Use the correct legume inoculant at 4 times the recommended rate when adding inoculant to a hydroseeder slurry. The mixture should be applied within one hour after mixing to reduce damage to seed.

Fertilizer should not be mixed with the seed-inoculant mixture because fertilizer salts may damage seed and reduce germination and seedling vigor. Fertilizer may be applied with a hydroseeder as a separate operation after seedlings are established.

### **Mulching**

The use of an appropriate mulch provides instant cover and helps ensure establishment of vegetative cover under normal conditions and is essential to seeding success under harsh site conditions (see the *Mulching Practice* for guidance). Harsh site conditions include the following: slopes steeper than 3:1 and adverse soils (soils that are shallow to rock, rocky, or high in clay or sand). Areas with concentrated flow should be treated differently and require a hydromulch formulated for channels or use of an appropriate erosion control blanket.

### **Verification of Installation**

Check materials and installation for compliance with specifications during installation of products.

### **Common Problems**

*Consult with a qualified design professional if the following occurs:*

Design specifications for seed variety, seeding dates or mulching cannot be met; substitutions may be required. Unapproved substitutions could lead to failure.

Seeding outside of the recommendations results in an inadequate stand. Reseed according to specifications of a qualified design professional (see recommendations under Maintenance).

### **Maintenance**

#### **Reseeding**

Inspect seedings weekly until a stand is established and at least monthly thereafter for stand survival and vigor. Also, inspect the site for erosion.

Eroded areas should be addressed appropriately by filling and/or smoothing, and a reapplication of lime, fertilizer, seed and mulch.

A stand should be uniform and dense for best results. Stand conditions, particularly the vegetative coverage, will determine the extent of remedial actions, such as seedbed preparation and reseeding. A qualified design professional should be consulted to advise on remedial actions. Consider no-till planting.

**Fertilizing**

If vegetation fails to grow, have the soil tested to determine whether its pH is in the correct range or whether nutrient deficiency is a problem.

Satisfactory establishment may require refertilizing the stand, especially if the planting is made early in the planting season. Follow soil-test recommendations or the specifications provided to establish the planting.

**Mowing**

Temporary plantings may be mowed and baled or simply mowed to complement the use of the site.

Millet, rye, and wheat may be mowed, but no lower than 6" (closer mowing may damage the stand).

Ryegrass is tolerant of most mowing regimes and may be mowed often and as close as 4" to 6" if this regime is started before it attains tall growth (over 8").

Bermuda grass is tolerant of most mowing regimes and can be mowed often and close, if so desired, during its growing season.

**References**

**Volume 1**

**Chapter 2**

Vegetation for Erosion and Sediment Control 2-10

**Chapter 4**

Land Grading (LG) 4-16

Topsoiling (TSG) 4-20

Mulching (MU) 4-48

Permanent Seeding (PS) 4-53

**Appendices Volume**

**Appendix G**

MDOT Vegetation Schedule G-1

## Dust Control (DC)



### Practice Description

Dust control includes a wide range of techniques that prevent or reduce movement of wind-borne soil particles (dust) during land disturbing activities. This practice applies to construction routes and other disturbed areas where on-site and off-site damage or hazards may occur if dust is not controlled.

### Planning Considerations

Construction activities that disturb soil can be a significant source of air pollution. Large quantities of dust can be generated, especially in “heavy” construction activities such as land grading for road construction and commercial, industrial, or subdivision development.

The scheduling of construction operations so that the least amount of area is disturbed at one time is important in planning for dust control.

The greatest dust problems occur during dry periods. Therefore, to the extent practicable, do not expose large areas of bare soil during drought conditions.

Where wind erosion is a potential cause of dust problems, preserving vegetation should be considered as a passive measure. Leave undisturbed buffer areas between graded areas wherever possible.

Installing temporary- or permanent- surface stabilization measures immediately after completing land grading will minimize dust problems.

## **Design Criteria and Construction**

Dust-control requirements should be designed by a qualified design professional and plans and specifications should be made available to field personnel prior to start of construction. Whenever possible, leave vegetated-buffer areas undisturbed between graded areas.

## **Scheduling**

Schedule construction operations so that the smallest area is disturbed at any one time.

## **Permanent Methods**

### ***Vegetative Cover***

For disturbed areas not subject to traffic, vegetation provides the most practical method of dust control. Establish vegetative cover according to the *Permanent Seeding* or *Temporary Seeding Practice*.

### ***Topsoiling***

This entails covering the surface with less erosive soil material. See *Topsoiling Practice* for guidance.

### ***Stone***

Stone used to stabilize construction roads can also be effective for dust control. Stone should be spread a minimum of 6" thick over construction roads in the disturbed area. For heavily traveled roads or roads subjected to heavy loads, the stone thickness should be 8" to 10". A non-woven geotextile meeting the requirements shown in the Table DC-1 for Class IV geotextiles should be used under the rock when the subgrade is soft or the blow count is less than 10.

## **Temporary Methods**

### ***Mulches***

Mulch offers a fast, effective means of controlling dust when properly applied. See *Mulching Practice* for guidelines on planning and installing the practice.

### ***Temporary Vegetative Cover***

For disturbed areas where no activity is anticipated for 14 days or longer, temporary seeding can effectively control dust. Establish vegetative cover according to *Temporary Seeding Practice* guidelines.

### ***Calcium Chloride***

Calcium chloride may be applied by mechanical spreader as loose, dry granules or flakes at a rate that keeps the surface moist, but not so high as to cause water pollution or plant damage. Sites may need to be retreated because the product degrades over time.

Table DC-1 Requirements for Nonwoven Geotextile

Property	Test method	Class I	Class II	Class III	Class IV <sup>1</sup>
Tensile strength (lb) <sup>2</sup>	ASTM D 4632 grab test	180 minimum	120 minimum	90 minimum	115 minimum
Elongation at failure (%) <sup>2</sup>	ASTM D 4632	≥ 50	≥ 50	≥ 50	≥ 50
Puncture (pounds)	ASTM D 4833	80 minimum	60 minimum	40 minimum	40 minimum
Ultraviolet light (% residual tensile strength)	ASTM D 4355 150-hr exposure	70 minimum	70 minimum	70 minimum	70 minimum
Apparent opening size (AOS)	ASTM D 4751	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>	As specified max. no.40 <sup>3</sup>
Permittivity sec-1	ASTM D 4491	0.70 minimum	0.70 minimum	0.70 minimum	0.10 minimum

Table copied from NRCS Material Specification 592.

<sup>1</sup> Heat-bonded or resin-bonded geotextile may be used for classes III and IV. They are particularly well suited to class IV. Needle-punched geotextile are required for all other classes.

<sup>2</sup> Minimum average roll value (weakest principal direction).

<sup>3</sup> U.S. standard sieve size.

### Spray-on Adhesives

Spray-on adhesives may be used on mineral soils for dust control. Traffic must be kept off treated areas to prevent the product from becoming ineffective. Examples of spray-on adhesives for use in dust control are listed in Table DC-2.

Table DC-2 Spray-on Adhesives for Dust Control on Mineral Soil

Material	Water Dilution	Type of Nozzle	Apply Gal/Ac
Latex Emulsion	12.5:1	Fine Spray	235
Resin In Water	4:1	Fine Spray	300

### Chemical Stabilization (CHS)

PAM may be used on mineral soils for dust control. Traffic must be kept off treated areas to prevent the product from becoming ineffective. The manufacturer or supplier shall provide written application methods for PAM and PAM mixtures. The application method shall ensure uniform coverage to the target and avoid drift to non-target areas including waters of the State. The manufacturer or supplier shall also provide written instructions to ensure proper safety, storage, and mixing of the product. Refer to the *Planning Considerations for Chemical Stabilization (PAM) Practice* for planning considerations before deciding to use this product.

**Sprinkling or Irrigation**

Sprinkling is especially effective for dust control on haul roads and other traffic routes. Sprinkle the site until the surface is wet. Repeat as needed. Also, bare areas may be kept wet with irrigation to control dust as an emergency treatment.

**Tillage**

Tillage is used to roughen the site and bring clods and moist soil to the surface. This is a temporary emergency measure that can be used on large, open, disturbed areas as soon as soil blowing starts. Begin tilling on the windward edge of the site. The depth of tillage is determined by the depth to moist soil and the amount of moist soil desired at the surface. In sandy soils, the depth to moist soil may make tillage impractical.

**Barriers**

A board fence, wind fence, sediment fence, hay bales, or similar barriers can control air currents and blowing soil. Place barriers perpendicular to prevailing air currents at intervals about 15 times the barrier height.



Figure 1 Sand Fence (<http://www.gulfmex.org/crp/7004/fence.jpg>)

**Street Cleaning**

Use a street sweeper to remove the source materials.

**Maintenance**

Check construction site during vehicular traffic or windy conditions to see if measures are working adequately. Maintain dust-control measures continuously throughout dry-weather periods, until all disturbed areas have been stabilized.


**References**

**BMPs from Volume 1**

**Chapter 4**

Topsoiling (TSG)	4-20
Chemical Stabilization (CHS)	4-25
Mulching (MU)	4-48
Permanent Seeding (PS)	4-53
Temporary Seeding (TS)	4-103

## Site Location Map

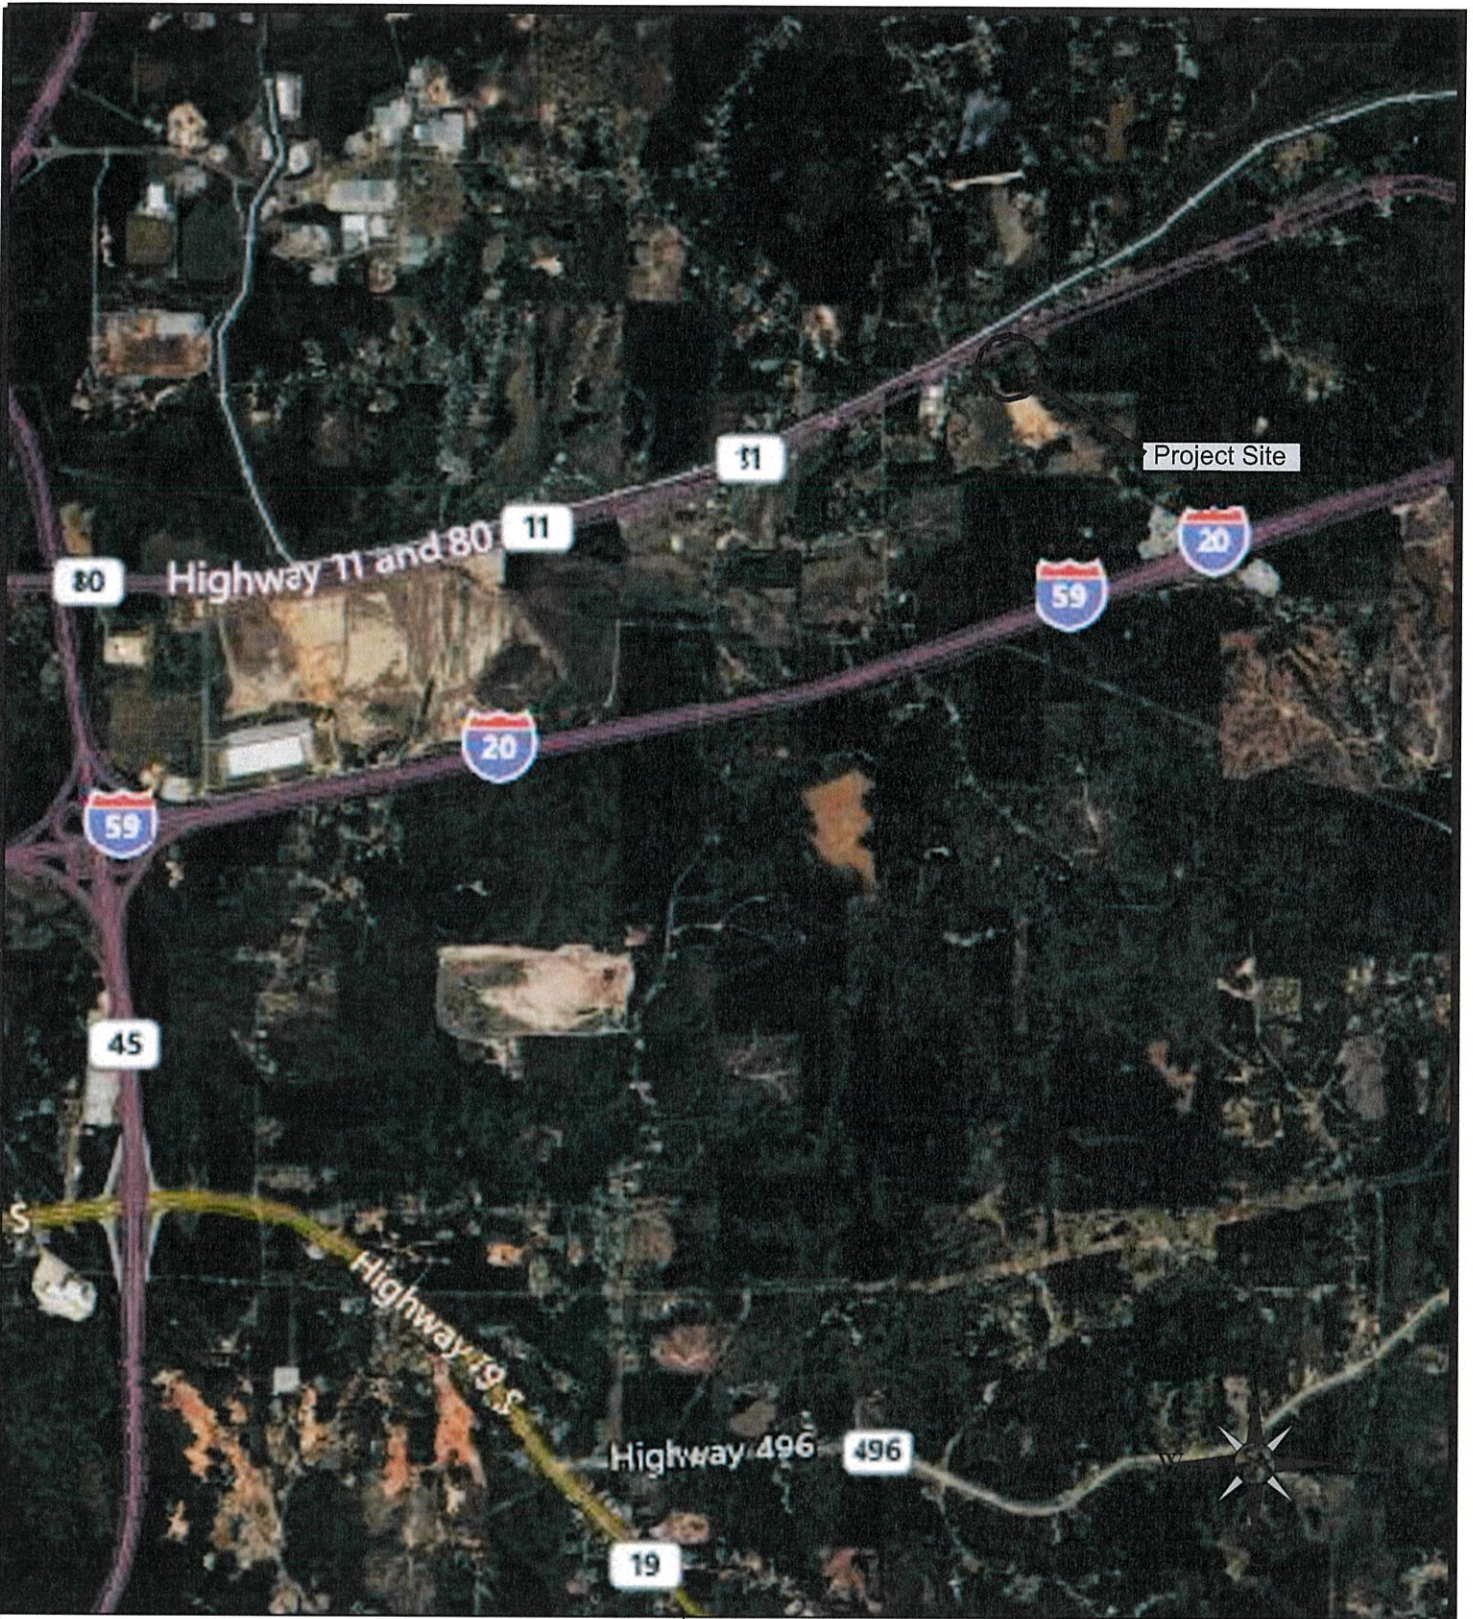

# Engineering Plus

Planning • Surveying • Testing • Landscape Design  
 1724-B 23rd Ave. Meridian, Mississippi 39301 (601) 693-4234  
 3662 Jefferson Street Macon, Mississippi 39341 (662) 726-1074  
 Email: engplus@engineeringplus.com

## SITE VICINITY MAP THE PINES OF MERIDIAN MERIDIAN, MS

MAP SOURCE: CIVIL3D

JOB NO: 24-304

DATE: 5-1-26

DRAWN BY: :LWL

CHECKED BY: RLA



Mississippi 811  
 CALL BEFORE YOU DIG  
 1-800-227-8477

Soil Survey of Lauderdale County, MS

Soil Map—Lauderdale County, Mississippi



Map Scale: 1:2,100 if printed on A portrait (8.5" x 11") sheet.



Map projection: Web Mercator Corner coordinates: WGS84 Edge ties: UTM Zone 16N WGS84

































Natural Resources Conservation Service

Web Soil Survey National Cooperative Soil Survey

5/1/2026 Page 1 of 3

## MAP LEGEND

- Area of Interest (AOI)**
  -  Area of Interest (AOI)
- Soils**
  -  Soil Map Unit Polygons
  -  Soil Map Unit Lines
  -  Soil Map Unit Points
- Special Point Features**
  -  Blowout
  -  Borrow Pit
  -  Clay Spot
  -  Closed Depression
  -  Gravel Pit
  -  Gravelly Spot
  -  Landfill
  -  Lava Flow
  -  Marsh or swamp
  -  Mine or Quarry
  -  Miscellaneous Water
  -  Perennial Water
  -  Rock Outcrop
  -  Saline Spot
  -  Sandy Spot
  -  Severely Eroded Spot
  -  Sinkhole
  -  Slide or Slip
  -  Sodic Spot
- Water Features**
  -  Streams and Canals
- Transportation**
  -  Rails
  -  Interstate Highways
  -  US Routes
  -  Major Roads
  -  Local Roads
- Background**
  -  Aerial Photography

## MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:20,000.

**Warning:** Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service  
 Web Soil Survey URL:  
 Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: Lauderdale County, Mississippi  
 Survey Area Data: Version 20, Sep 8, 2025

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Jan 3, 2021—May 8, 2021


The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

## Map Unit Legend

Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
Ja	Jena fine sandy loam, 0 to 2 percent slopes, frequently flooded	7.2	44.4%
PtA	Prentiss fine sandy loam, 0 to 2 percent slopes	5.7	35.2%
SW	Sweatman association, 5 to 35 percent slopes	3.3	20.4%
<b>Totals for Area of Interest</b>		<b>16.3</b>	<b>100.0%</b>





# Quadrangle Maps

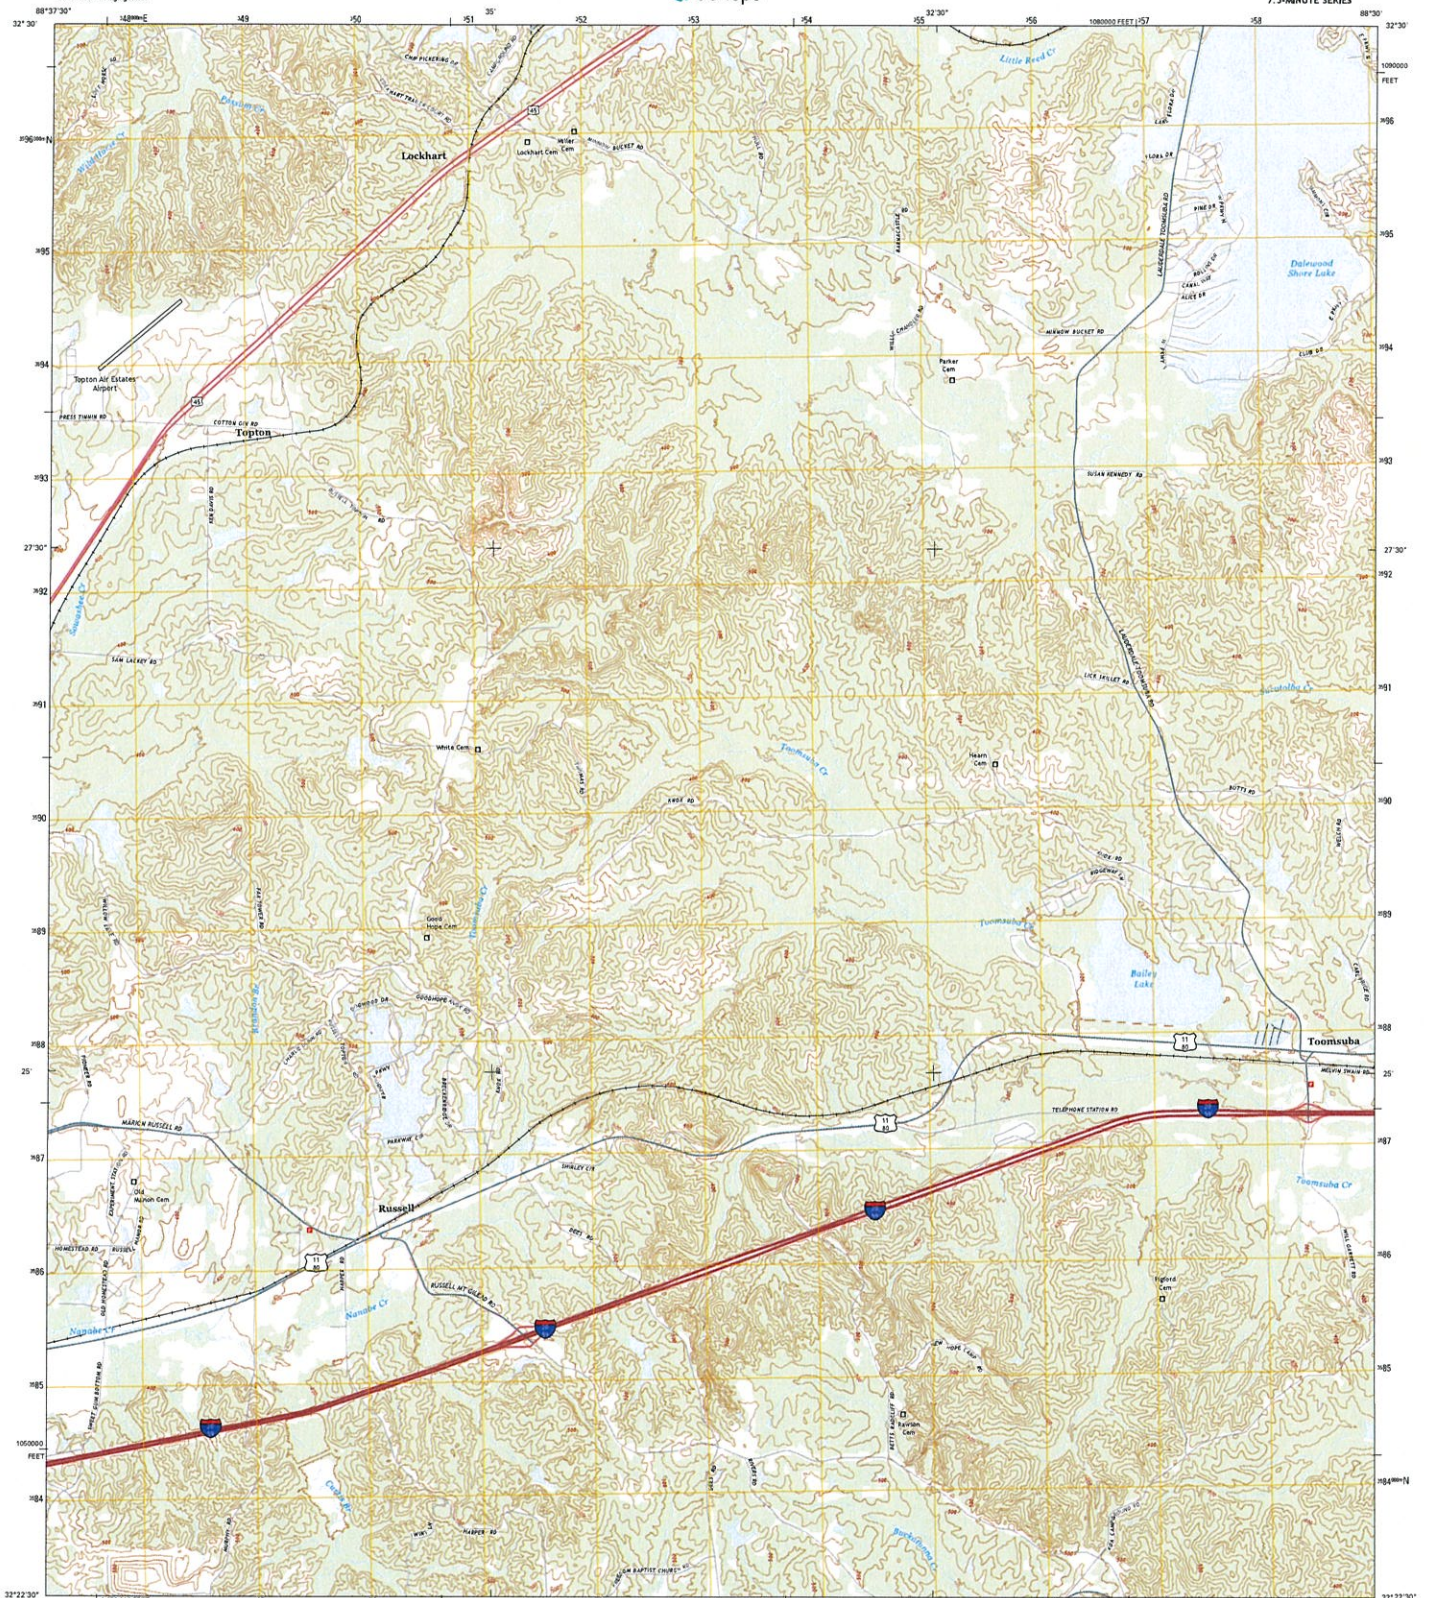

Produced by the United States Geological Survey  
North American Datum of 1983 (NAD83)  
North American Datum of 1983 (NAD83). Projection and  
Horizontal datum: Universal Transverse Mercator, Zone 16S  
10-degree grid. Vertical datum: Mean Sea Level, 1929  
10-degree grid. Mississippi Coordinate System of 1983 (last  
issue).

This map is not a legal document. Boundaries may be  
generalized for this map scale. Private lands within government  
reservations may not be shown. Obtain permission before  
entering private lands.

Boundary: NAD 2011 July 2014  
Road: NAD 2011 July 2014  
Name: NAD 2011 July 2014  
Hydrography: National Hydrography Dataset, 2014  
Contour: National Elevation Dataset, 2014  
Boundary: Multiple sources; see metadata file 3072-2015  
Public Land Survey System: BLM, 2015



ROAD CLASSIFICATION

Expressway	Local Connector
Secondary Hwy	Local Road
Ramp	AWD
Interstate Route	US Route
	State Route

1	2	3
4	5	6
7	8	9

- 1 Deltavia
- 2 Lauderdale
- 3 Tumbalo
- 4 Meridian North
- 5 Newbern
- 6 Meridian South
- 7 Winona
- 8 Winton



Erosion Control Plan



Mississippi 811  
**CALL BEFORE YOU DIG**  
 1-800-227-8477

Prior to any demolition or excavation it shall be the Contractor's responsibility to notify Mississippi One-Call Center for utility line locations.  
 1-800-227-8477  
 601-852-4874  
 MS1call.org

It shall be the Contractor's responsibility to maintain any & all markings needed to protect existing utilities. Any damage or interruption of service shall be reported immediately to the appropriate utility company. Contractor shall be responsible for repair and restoration of service in full cooperation and in full compliance with the affected utility company. Any cost associated with such repairs shall be at the Contractor's expense. Refer to Mississippi811.org for terms of location.

WORKED AREAS TO THE SHORTEST AMOUNT OF AROUND DISTURBED AREAS OF SITE WHENEVER POSSIBLE. DISTURBED AREAS AS SOON AS THEY BECOME AVAILABLE.

BEST MANAGEMENT PRACTICES DESIGNED TO REMOVE SEDIMENT FROM EROSION IN ACCORDANCE WITH MS DEPARTMENT OF TRANSPORTATION REGULATIONS. BMP'S SHALL BE PLACED IN SCHEDULED AND LAND DISTURBING ACTIVITIES. COMMENCING ANY LAND DISTURBANCE SHALL INCLUDE SILT FENCE ALONG THE PERIMETER OF THE DISTURBED AREA. INSTALLATION OF DIVERSION DITCHES OR DIKES AS NEEDED TO PREVENT EROSION. CHECKS SHALL BE INSTALLED AS NEEDED TO PREVENT OVERFLOW OF WATER. BARRIERS SHALL BE DE-SILTED WHEN NECESSARY.

OPERATIONS PROGRESS, CONTRACTOR SHALL PROVIDE DEVICES SUCH AS CHECK DAMS, SILT FENCE, SILT TRAPS, AND OTHER PREFABRICATED DEVICES. DISTURBED AREAS SHALL BE RESTORED TO ORIGINAL OR BETTER CONDITION. PERMANENT EROSION CONTROL SHALL BE INSTALLED AS SHOWN ON PLANS. TEMPORARY EROSION CONTROL DEVICES SHALL BE INSTALLED AS SHOWN ON PLANS.

TEMPORARY BMP CONTROLS AS NEEDED TO PREVENT EROSION FROM AFFECTING DOWNSTREAM PROPERTY THROUGHOUT THE DISTURBED AREA. VEGETATION AND/OR VEGETATIVE AND STRUCTURAL EROSION CONTROL MEASURES SHALL BE INSTALLED TO MINIMIZE OFF-SITE IMPACTS.

MEASURES USED TO MITIGATE ADVERSE IMPACTS FROM CONSTRUCTION SHALL BE LIMITED TO SILT FENCING, SEDIMENT TRAPS, SWALES AND OTHER PREFABRICATED DEVICES.

ACQUIRING ALL NECESSARY PERMITS. THIS MAY INCLUDE THE MISSISSIPPI DEPARTMENT OF TRANSPORTATION FOR ALL RECORD KEEPING AND PERMITS.



VERIFY THE ACTUAL DISTURBED AREA THROUGH VISUAL SURVEY, CONSTRUCTION PARKING, AND OTHER CONSTRUCTION OPERATIONS.

CONSTRUCTION SHALL BE BASED ON ACTUAL DISTURBED AREA.

NOTIFICATION OF THE SMALL CONSTRUCTION NOTICE (SCN) EVENT PLAN (SWPPP). A SWPPP MUST BE DEVELOPED AND A COPY MUST BE SUBMITTED TO DEQ FOR APPROVAL AND A COPY MUST BE RETAINED ON SITE AT ALL TIMES.

OTHER DEVICES SPECIFICALLY DESIGNED FOR EROSION CONTROL ARE ACCEPTABLE.

INSTALL ADDITIONAL CONTROLS AS NEEDED TO PREVENT EROSION. EXISTING PAVEMENTS SHALL BE CLEANED AND REPAIRED AS NEEDED.

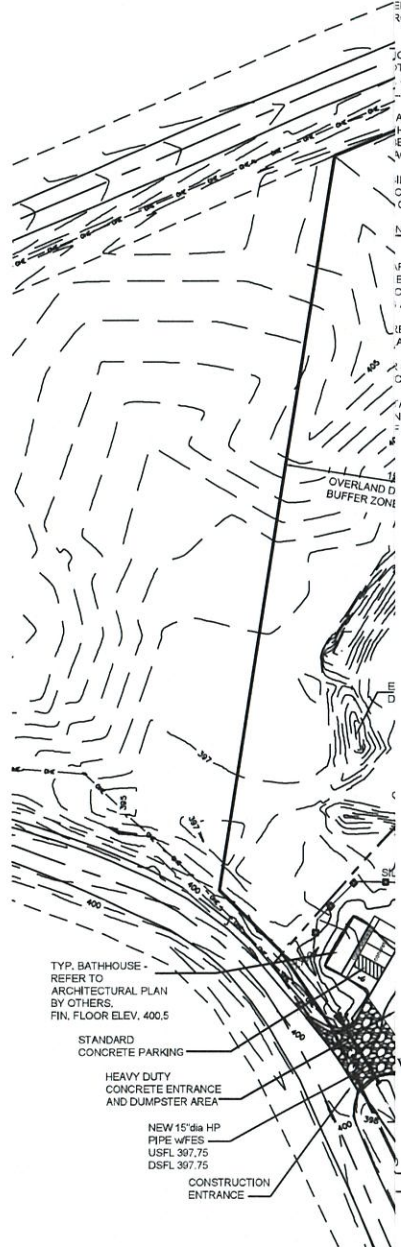

**Engineering Plus**  
 Planning • Surveying • Testing • Landscape Design  
 17242 2nd Ave., Trask, Arkansas 72781 (501) 852-2342  
 Arkansas State Union, Batesville 3934 (501) 754-1114 (Fax)  
 ep@epengineeringplus.com

THE PINES OF MERIDIAN  
 RUSSELL, MS  
 FOR LOTUS PINES, LLC

SEAL

NO.	REVISION	DATE

DATE 4-17-28  
 EP PROJ NO. 24-304  
 DWG FILE  
 v04f2c4e3028f4a1e2028124-304  
 NANABE RV PARK - PINE  
 BELTICAD24-304 NANABE RV  
 SITE 5-1-26

SHEET TITLE  
**STORM  
 WATER  
 SUBMITTAL**

SHEET NO.  
**SW1.0**



Engineering Plus

Planning • Surveying • Testing • Landscape Design  
17248 27th Ave., Jackson, Mississippi 39211 (601) 954-2244 FAX  
jackson@ep-engineering.com

THE PINES OF MERIDIAN  
RUSSELL, MS  
FOR LOTUS PINES, LLC

SEAL

NO.	REVISION	DATE

DATE 4-17-20


EP PROJ NO. 24-304  
DWG FILE  
\\EP-CAD\ESD\Projects\24-304\24-304  
NANABE RV PARK- PINE  
BELT\CAD\24-304 NANABE RV  
SITE 5-1-20

SHEET TITLE

STORM  
WATER  
SUBMITTAL  
DETAILS

SHEET NO.


SW1.1

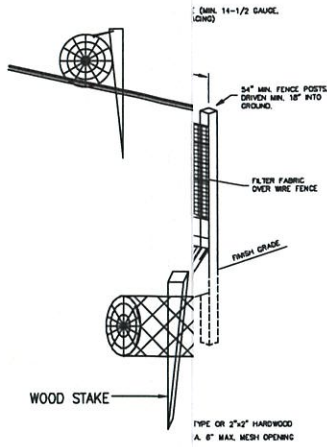

- GENERAL NOTES:
1. INSTALL PER MANUFACTURER'S INSTRUCTIONS
  2. REFER TO EROSION CONTROL MANUAL FOR EROSION CONTROL MEASURES
  3. MAKE SURE WATER TO FLOW BENEATH FILTER FABRIC
  4. SECURE WATTLE WITH STAKES

SEE

D MATERIAL



PROVIDE FULL WIDTH OF GRASS/EGRESS AREA

PROTECTION
